



AGENDA

Consolidated Technology Services • WA

State Data Center Agency Implementation Coordinator Meeting

October 22th, 2015

2:00 – 3:00 p.m.

Attendees: SDC Project Staff and Agency Implementation Coordinators

Time	Topic	Presenter
2:00 – 2:10	Welcome & Introductions	All
2:10 – 2:35	Update on SDC Projects	Heidi Brownell
2:35 – 3:00	Q&A	All
3:00 p.m.	Adjourn	

Additional Instructions:

- **Meeting Location -** 1500 Jefferson Building [[PDF Map](#) or [Mapped with Google](#)]
Conference Room 2208

State Data Center (SDC)
*Agency Implementation Coordinator
Meeting*


October 22, 2015

Agenda

- Welcome – Introductions/Review Agenda
- Update on SDC Projects
- Customer Communications
- Q&A

SDC Projects

SDC Projects Timeline

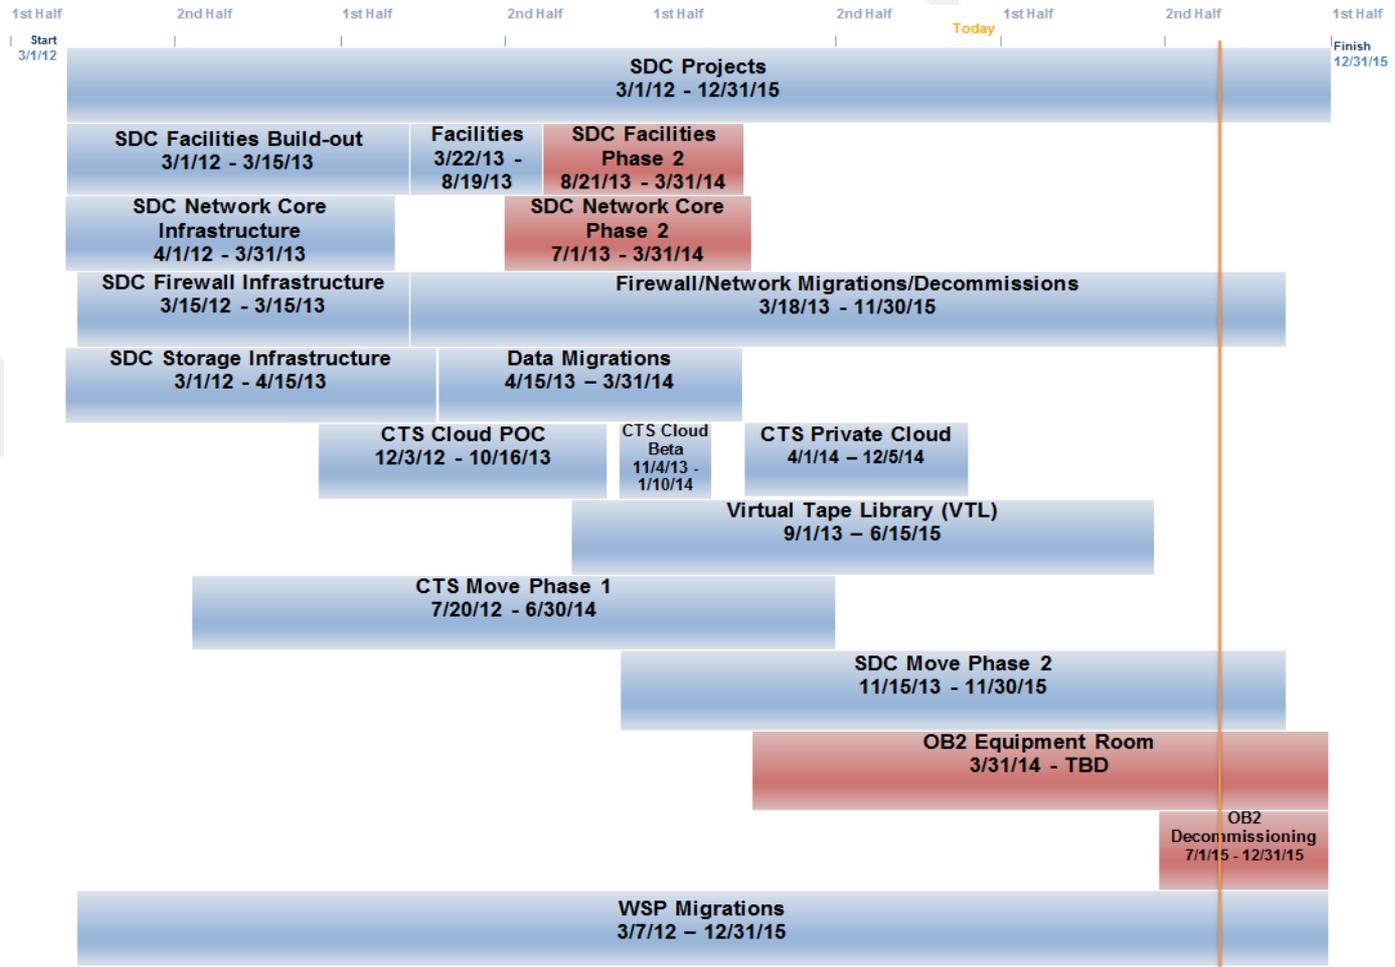

The IT partner of choice for agencies in Washington state

SDC Firewall Project

Firewall Migrations

Recent:


- N/A

Upcoming:

- Prepare to decommission remaining four firewalls

No Change

Firewall Migrations

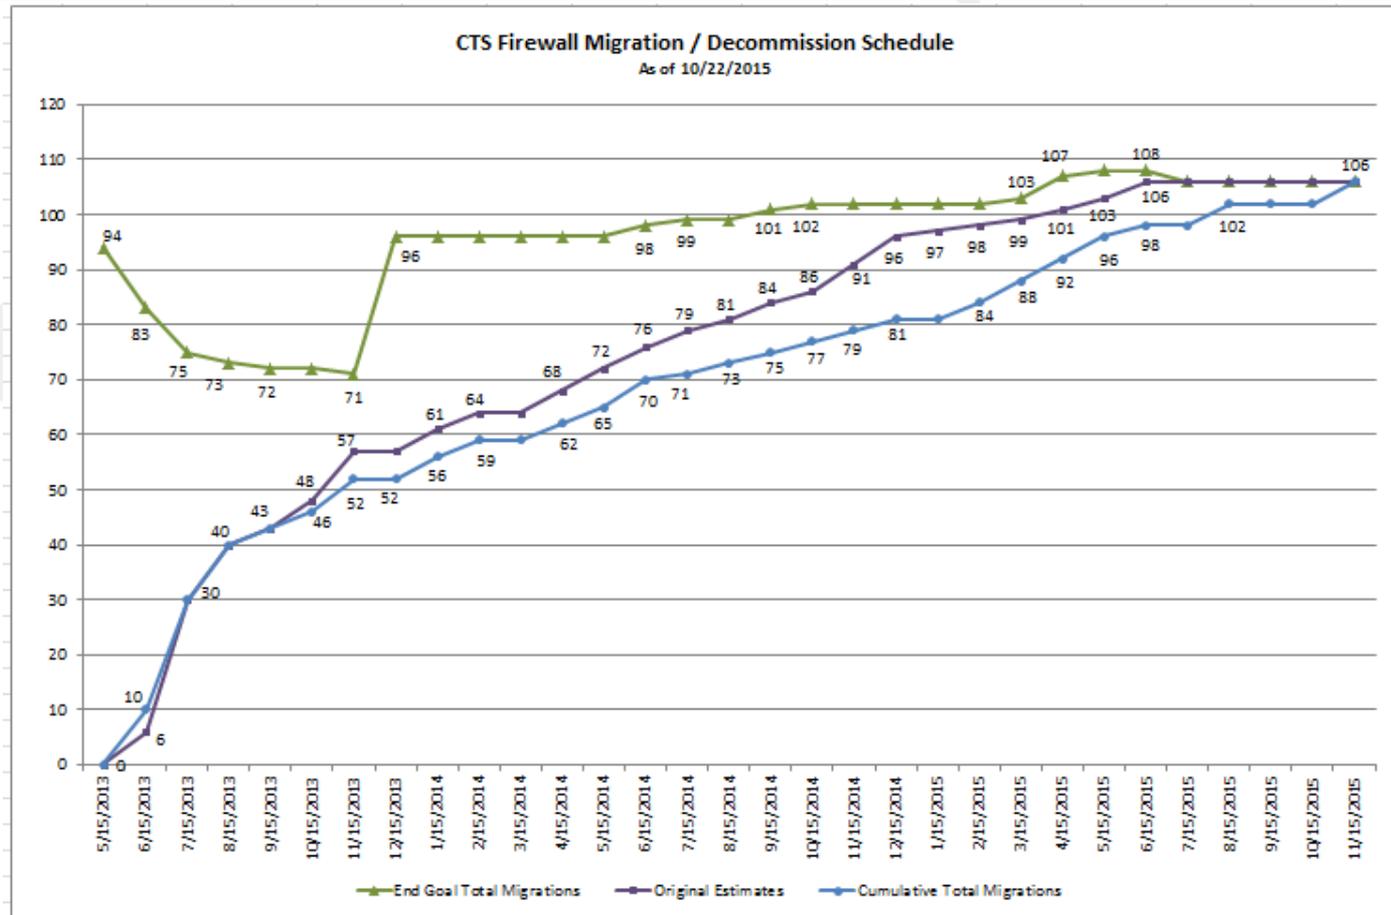

SDC Move Phase 2

SDC Move Ph 2- CTS Devices

Recent:

- DES continued with installation of new security system in OB2

Upcoming:

- Complete Decomm Group 27 upon successful completion of new security system installation

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

SDC Move Ph 2- Security

IPSEC Site-to-Site/Branch Office

Recent:

- Migrated DOC and DOL branch office sites

Upcoming:

- Perform final migrations from OB2
 - Asotin County Branch Office
 - WSP-to-DOJ/ATF Branch Office
- Migrate the VPN concentrator to SDC on Nov 18th
- Transfer final migrations to OPs team

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

SDC Move Ph 2– Network

Migrate Access Layer and 6509s to SDC

Recent:

- Completed 16 migrations

Upcoming:

- Perform additional migrations (final migrations must wait for PRINT and Security system migrations)

Total # Remaining

57

Total # Connections

716

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

SDC Move Ph 2 - Customers

Recent:

- Completed DSHS decommissioning activities

Upcoming:

- Project complete!

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations



WSP

The IT partner of choice for agencies in Washington state

WSP

Recent:

- Conducted review of remaining work sprints
- Supported 2 circuit installations in SDC
- Supported cabling request

Upcoming:

- Continue to support WSP

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

OB2 Equipment Rm

OB2 Equipment Room

DES, CTS, and DSHS have been meeting to discuss the requirements, plan, and design of the future state of vacated data center space in OB2. Some Telephony and LAN equipment will need to stay in OB2 to support the tenants.

Recent:

- No activity

Upcoming:

- DSHS decision on telephony direction

OB2 Decommissioning

Vendor Trunk Migrations

Recent:

- Completed one migration
- Developed migration options for the four remaining circuits

Upcoming:

- Complete one additional migration
- Work with the vendor to agree on best option for remaining migrations

Total # Remaining	5
Total # Circuits	335

Campus Fiber Network

Recent:

- Analyzed trunks for accurate count of connections and adjusted target
- Completed 312 connection migrations
- Worked with impacted customers to schedule remaining migrations

Upcoming:

- Perform migrations on October 31st, November 7th & 14th
- Continue to work with customers to confirm migrations

Total # Remaining


408

Total # Connections

720

Campus Fiber Network Activity Pipeline

DRAFT

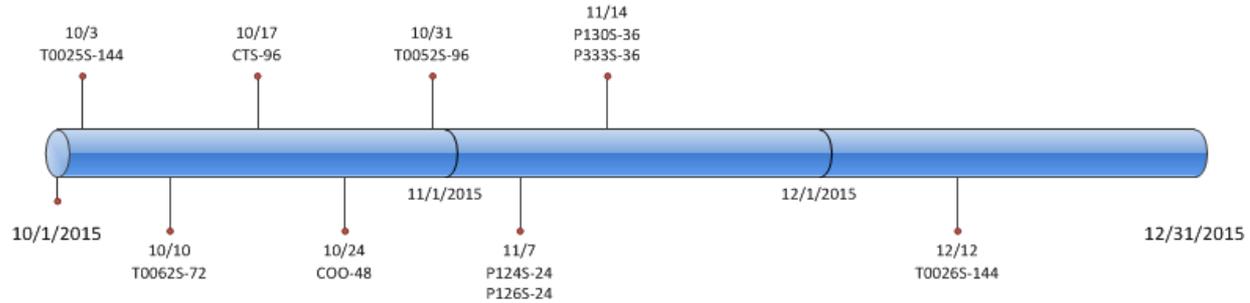

Customer Expectations

- Customers will be contacted prior to the target move date to set the schedule.
- Customer approves schedule, establishes test scenarios, performance benchmarks and prepares for move.
- Customer Coordination continues through entire move cycle.
- Customer gives final acceptance of move completion.

CFN Migrations

T00255-144	T0625-72	CTS-96	COO-48	T00525-96
<ul style="list-style-type: none"> • COM • CTS • DES • DOP • DSHS • WaTech LTS 	<ul style="list-style-type: none"> • AGR • DFW • RCO 	<ul style="list-style-type: none"> • ARTS • DEL • DES • DSHS • HUM • DOT • OPD • PDC • SOS • TIB • ACB • WaTech LTS • WTECB 	<ul style="list-style-type: none"> • N/A 	<ul style="list-style-type: none"> • CTS • DEL • DES • DOT • DSHS • SOS • TIB • WaTech LTS • WTECB
P1245-24	P1265-24	P1305-36	P3335-36	T00265-144
<ul style="list-style-type: none"> • CFC • DAHP • SOS • WaTech LTS 	<ul style="list-style-type: none"> • DOL 	<ul style="list-style-type: none"> • DNR • DOT • WaTech LTS 	<ul style="list-style-type: none"> • CTS • DES • SAO • WaTech LTS 	<ul style="list-style-type: none"> • CTS • DES • DOL • DOT • DSHS • SAO • SOS • WaTech LTS

OB2 SMON Node Relocation

This project will move customer connections to the OB2 Node to another node.

Recent:

- Completed PERC and DNR migrations
- Cancelled DOL migration

Upcoming:

- Reschedule DOL migration
- Schedule LEG Node Reconfiguration

Total # Remaining

3

Total # Connections

18

Move Telephony Equipment

Recent:

- Continued decommissioning enclosures that aren't needed for DSHS

Upcoming:

- Complete OB2 Voice Network Interim Migration

Customer Communications

Customer Communications

- The [SDC Projects website](#) provides information regarding project background, status, meeting information, and migration resources.
- The [SDC Migration Calendar](#) provides a calendar view of migration information linking back to the Technical Bulletins.
- [Technical Bulletins](#) notify customers of upcoming changes regarding SDC project-related changes.
- The [SDC Project ASK](#) website provides online document collaboration regarding agency migrations out of OB2.
- Monthly AIC meetings provide an opportunity to hear status presented and ask questions.
- Migration project meetings are scheduled with specific customers as needed to prepare for their migrations.

SDC Project Website

The [SDC Projects](#) website provides current information about the status of the projects.

See also: [Customer Readiness website](#)

The screenshot shows the SDC Project Website interface. At the top left is the CTS logo and a quote: "CTS' Exchange 2010 environment called out as one of the best evaluated! Read more". A search bar is in the top right. The navigation menu includes Home, Products and Services, and Projects. Below the menu are links for Cloud Based Email Collaboration, Shared Services Email, and State Data Center. The main content area is titled "State Data Center Projects" and dated April 30, 2014. It features sections for "SDC Move Phase 2" (customer migration meetings), "CTS Move Phase 1" (high level accomplishments like Fortress migration and server moves), "Network and Firewalls" (98 firewalls identified, 42 migrated), and "Facilities/Network Core Phase 2" (readiness for customers). An "Important Links" sidebar lists Home, Customer Readiness, Background, Status Report Archive, Meetings, Migration Calendar, and Archived Updates. At the bottom, there are two summary boxes: "BUDGET: SDC Projects Spending Plan" with a bar chart titled "SDC Projects Lifecycle Budgets and Actuals" and a note about baseline budget and actuals; and "STATUS: Current Status Report" with a table showing progress for SDC Program, OB2 Heat Reduction, SDC Facilities, and SDC Network Core.

SDC Projects	Scope	Sched	Budget
SDC Program	●	●	●
OB2 Heat Reduction	(completed)		
SDC Facilities	(completed)		
SDC Network Core	(completed)		


Migration Calendar Updates

Customers on the SGN can view migration events on the [SDC Migration Calendar](#).

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1) SDC Move Ph 2- Security LNI/HCA VIPS Migration	2)	3) Campus Fiber Network Migration: T0025S
4)	5)	6)	7) SDC Move Ph 2- Security DSHS HBE Migration OB2 SMON Node Relocation: DNR	8)	9)	10) Campus Fiber Network Migration: T0062S-72
11)	12)	13) SDC Move Ph 2- Security DOL to CIS Migration SDC Move Ph 2- Security DOC Davenport Migration	14) SDC Move Ph 2- Security DOC Spokane Migration	15)	16)	17) DES PRINT Relocation Campus Fiber Network Migration: CTS-96
18) OB2 SMON Node Relocation: DOL	19)	20) SDC Move Ph 2- Security DOC Gig Harbor Migration	21)	22)	23)	24)
25)	26)	27)	28)	29)	30)	31) Campus Fiber Network Migration: T0052S-96

SDC Project ASK Website

The [SDC Projects ASK](#) website enables customer and CTS collaboration regarding the migrations.



The screenshot shows the 'SDC Projects' website interface. At the top, there is a navigation bar with 'Consolidated Technology Services' on the left and 'CTS Sites', 'Newsfeed', 'SkyDrive', and 'Site' on the right. Below the navigation bar, the 'BROWSE PAGE' section is visible. The main content area features the 'Agency Shared Knowledge' logo and the title 'SDC Projects'. A left-hand navigation menu includes 'Home', 'Documents', 'All General Information', and 'ATG Documents'. The main content area contains several sections: 'Home' with a description of the CTS ASK SharePoint environment; 'Documents' with a description of the site's purpose for managing migrations; 'Other Pages' with links to 'SDC Projects' and 'SDC Migration Calendar'; and 'UPDATES' with a recent update dated 3/19 regarding a customer kick-off meeting. A search box is located in the top right corner. A large red note is overlaid at the bottom of the screenshot.

Note: Site access is provided to current migration customers.

Q&A



The IT partner of choice for agencies in Washington state

Next Meeting

Our next meeting will be **November 19th** 2:00 – 3:00 p.m.

This is a change from our typical fourth Thursday schedule!

All meetings will be held at [1500 Jefferson Building](#).

Our online [Meeting Calendar](#) is continually updated with meeting materials.

Contact Information

- Doug Wood – CTS Project Manager
Doug.Wood@watech.wa.gov 360.407.8631
- Senthil Masilamani – CTS Project Manager
Senthil.Masilamani@watech.wa.gov 360.407.8635
- Heidi Brownell – CTS Chief Project and Planning Officer
Heidi.Brownell@watech.wa.gov 360.407.8980
