

## State Data Center Agency Implementation Coordinator Meeting

November 17<sup>th</sup>, 2015

2:00 – 3:00 p.m.

**Attendees:** SDC Project Staff and Agency Implementation Coordinators

Time	Topic	Presenter
2:00 – 2:10	Welcome & Introductions	All
2:10 – 2:35	Update on SDC Projects	Heidi Brownell
2:35 – 3:00	Q&A	All
3:00 p.m.	Adjourn	

### Additional Instructions:

- **Meeting Location -** 1500 Jefferson Building [[PDF Map](#) or [Mapped with Google](#)]  
Conference Room 2208

State Data Center (SDC)  
*Agency Implementation Coordinator  
Meeting*


November 17, 2015

# Agenda

- Welcome – Introductions/Review Agenda
- Update on SDC Projects
- Customer Communications
- Q&A

# SDC Projects

# SDC Projects Timeline

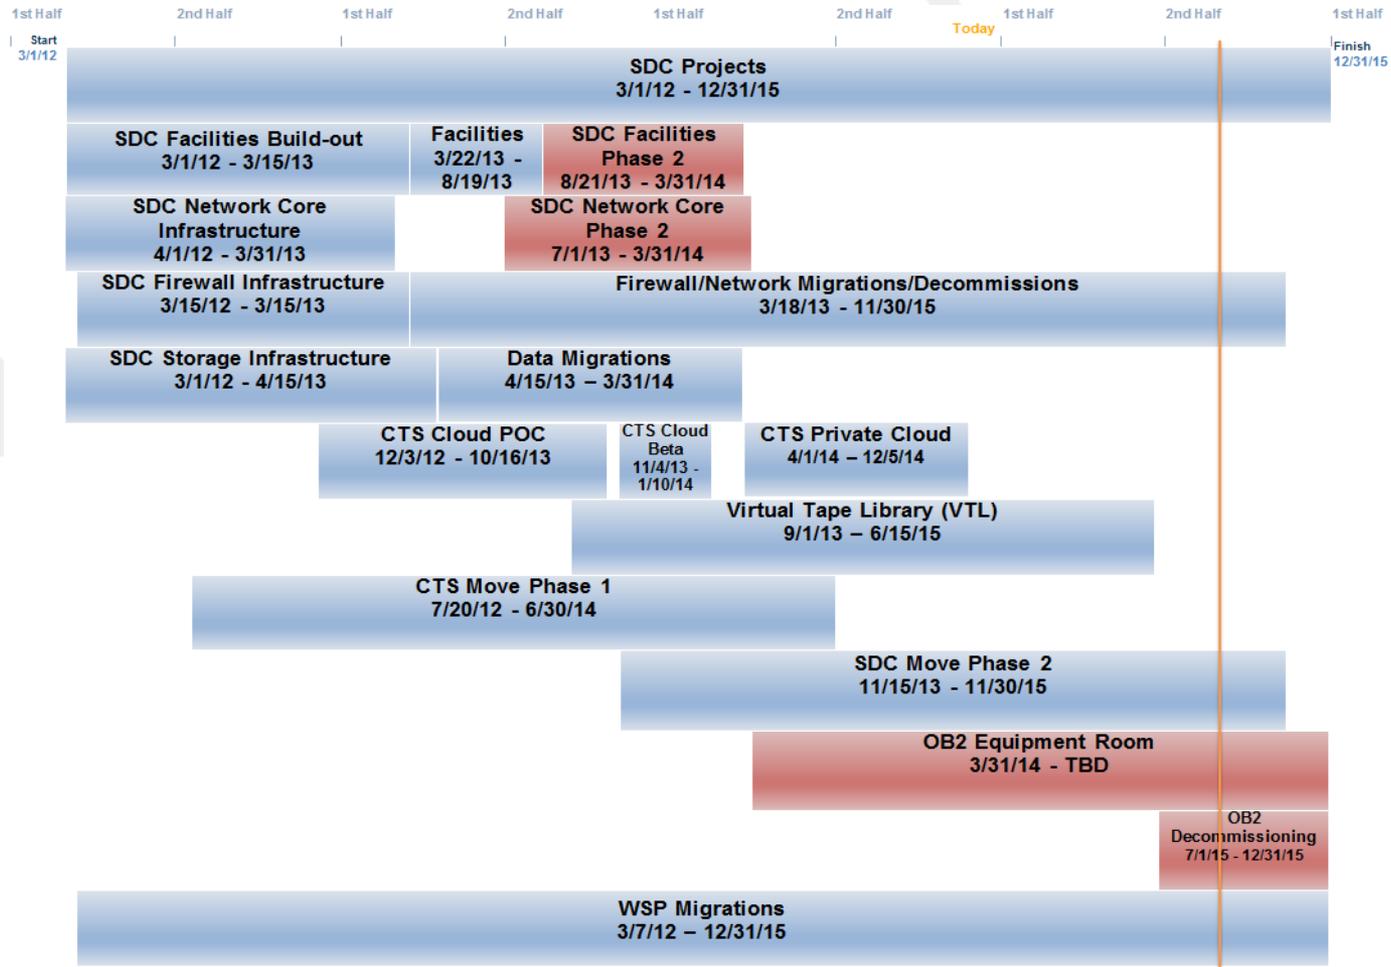

The IT partner of choice for agencies in Washington state

# SDC Firewall Project

# Firewall Migrations

## Recent:


- N/A

## Upcoming:

- Prepare to decommission remaining four firewalls

*No Change*

# Firewall Migrations

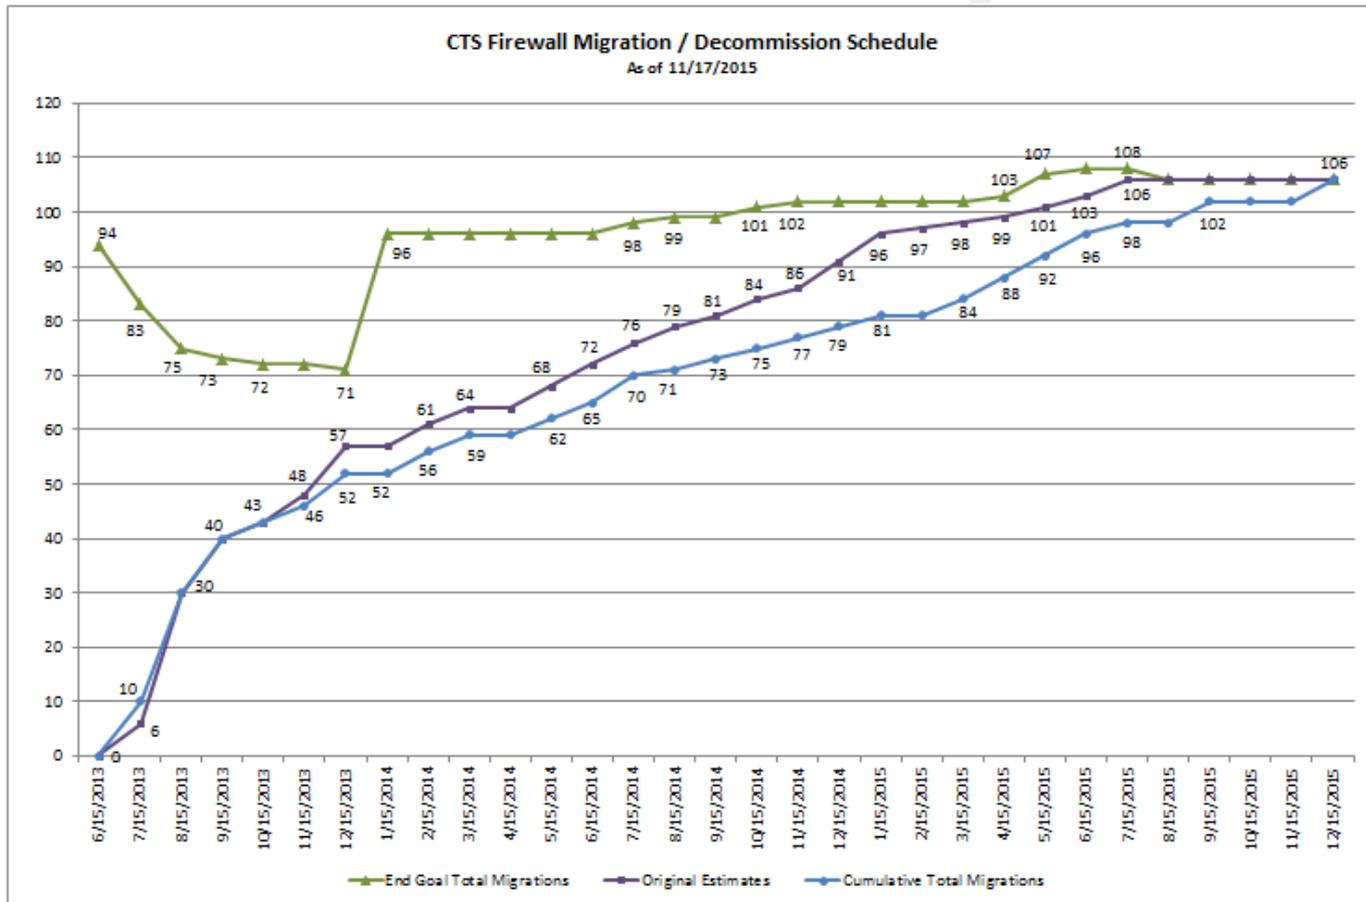

# SDC Move Phase 2

# SDC Move Ph 2- CTS Devices

## Recent:

- Completed Decom Group 27

## Upcoming:

- The remaining equipment in OB2 is supporting DES Print

## SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

# SDC Move Ph 2- Security

## IPSEC Site-to-Site/Branch Office

### Recent:

- Performed final migrations from OB2

### Upcoming:

- Migrate the VPN concentrator to SDC on Nov 18<sup>th</sup>
- Transfer final migrations to OPs team

## SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

# SDC Move Ph 2– Network

## Migrate Access Layer and 6509s to SDC

### Recent:

- Completed 4 migrations

### Upcoming:

- Perform additional migrations (final migrations must wait for PRINT and Security system migrations)

Total # Remaining

53

Total # Connections

716

## SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations



WSP

The IT partner of choice for agencies in Washington state

# WSP

## Recent:

- Completed facility design and issued colocation quote for new scope of work

## Upcoming:

- Continue to support installation in the SDC

## SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

# OB2 Equipment Rm

# OB2 Equipment Room

DES, WaTech, and DSHS have been meeting to discuss the requirements, plan, and design of the future state of vacated data center space in OB2. Some Telephony and LAN equipment will need to stay in OB2 to support the tenants.

## Recent:

- Reviewed updated design documents
- DSHS decision on telephony

## Upcoming:

- Continue supporting DES if/when requested

# OB2 Decommissioning

# Vendor Trunk Migrations

## Recent:

- Completed one migration
- Developed migration options for the four remaining circuits

## Upcoming:

- Schedule work with vendor to migrate four remaining circuits to SDC

Total # Remaining	4
Total # Circuits	335

# Campus Fiber Network

## Recent:

- Worked with impacted customers to confirm migrations
- Performed migrations on October 31<sup>st</sup> and November 7<sup>th</sup>

## Upcoming:

- Reschedule Migrations that were originally scheduled for Nov 14<sup>th</sup>
- Finalize planning for Dec migration (if necessary)


Total # Remaining

216

Total # Connections

720

# Campus Fiber Network Activity Pipeline

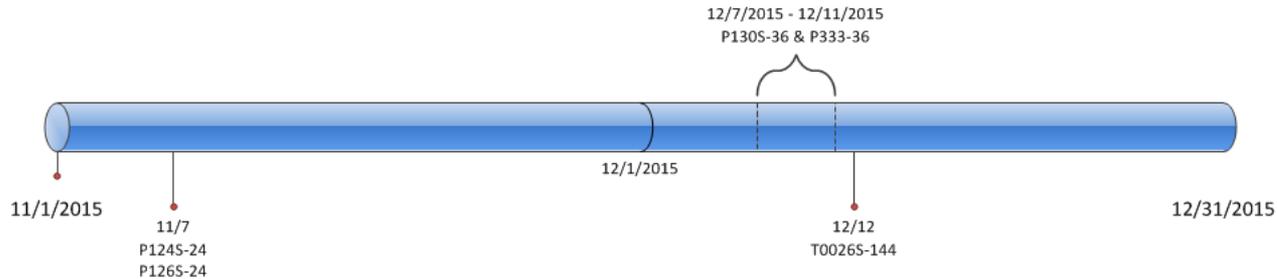

## Customer Expectations

- Customers will be contacted prior to the target move date to set the schedule.
- Customer approves schedule, establishes test scenarios, performance benchmarks and prepares for move.
- Customer Coordination continues through entire move cycle.
- Customer gives final acceptance of move completion.

### Completed P124S-24

- CFC
- DAHP
- SOS
- WaTech LTS

### Completed P126S-24

- DOL

### Pending Rescheduling P130S-36

- DNR
- DOT
- WaTech LTS

### Pending Rescheduling P333S-36

- CTS
- DES
- GOV
- LSC
- OFM
- SAO
- WaTech LTS

### T0026S-144

- |           |              |
|-----------|--------------|
| • COMCAST | • DSHS       |
| • CTS     | • SAO        |
| • DES     | • SOS        |
| • DOL     | • WaTech LTS |
| • DOT     |              |

# OB2 SMON Node Relocation

This project will move customer connections in the OB2 Node to another node.

## Recent:

- Completed DOL MPLS migration
- Rescheduled DOL SGN Migration
- Scheduled LEG Node Reconfiguration

## Upcoming:

- Perform DOL SGN Migration on November 24<sup>th</sup>
- Perform LEG Node Reconfiguration on December 6<sup>th</sup>

**Total # Remaining**

**2**

**Total # Connections**

**18**

# Move Telephony Equipment

## Recent:

- Continued decommissioning enclosures that aren't needed for DSHS

## Upcoming:

- Continue decommissioning enclosures
- Perform OB2 Voice Network Interim Migration on December 5<sup>th</sup>

# Customer Communications

# Customer Communications

- The [SDC Projects website](#) provides information regarding project background, status, meeting information, and migration resources.
- The [SDC Migration Calendar](#) provides a calendar view of migration information linking back to the Technical Bulletins.
- [Technical Bulletins](#) notify customers of upcoming changes regarding SDC project-related changes.
- The [SDC Project ASK](#) website provides online document collaboration regarding agency migrations out of OB2.
- Monthly AIC meetings provide an opportunity to hear status presented and ask questions.
- Migration project meetings are scheduled with specific customers as needed to prepare for their migrations.

# SDC Project Website

The [SDC Projects](#) website provides current information about the status of the projects.

See also:  
[Customer Readiness website](#)

The screenshot shows the SDC Project Website interface. At the top left is the CTS logo and a quote: "CTS' Exchange 2010 environment called out as one of the best evaluated! Read more". A search bar is on the top right. The navigation menu includes Home, Products and Services, and Projects. Below the menu are links for Cloud Based Email Collaboration, Shared Services Email, and State Data Center. The main content area is titled "State Data Center Projects" and dated "April 30, 2014". It features sections for "SDC Move Phase 2" (customer migration meetings), "CTS Move Phase 1" (high level accomplishments like Fortress migration and server moves), "Network and Firewalls" (98 firewalls identified, 42 migrated), and "Facilities/Network Core Phase 2" (readiness for customers). An "Important Links" sidebar lists Home, Customer Readiness, Background, Status Report Archive, Meetings, Migration Calendar, and Archived Updates. At the bottom, there are two summary boxes: "BUDGET: SDC Projects Spending Plan" with a bar chart titled "SDC Projects Lifecycle Budgets and Actuals" and a note about baseline budget and actuals; and "STATUS: Current Status Report" with a table showing progress for SDC Program, OB2 Heat Reduction, SDC Facilities, and SDC Network Core.

SDC Projects	Scope	Sched	Budget
SDC Program	●	●	●
OB2 Heat Reduction		(completed)	
SDC Facilities		(completed)	
SDC Network Core		(completed)	

# Migration Calendar Updates


Customers on the SGN can view migration events on the [SDC Migration Calendar](#).

November 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1)	2)	3)	4)	5)	6)	7) Campus Fiber Network Migration: P124S-24 & P126S- 24
8)	9)	10)	11)	12)	13)	14)
15)	16)	17)	18) Physical Move of Site -to-Site Cisco IPSEC VPN Concentrator	19)	20)	21)
22)	23)	24) OB2 SMON Node Relocation: DOL	25)	26)	27)	28)
29)	30)					

# SDC Project ASK Website

The [SDC Projects ASK](#) website enables customer and CTS collaboration regarding the migrations.



The screenshot shows the 'SDC Projects' website interface. At the top, there is a navigation bar with 'Consolidated Technology Services' on the left and 'CTS Sites', 'Newsfeed', 'SkyDrive', and 'Site' on the right. Below the navigation bar, the 'BROWSE PAGE' section is visible. The main content area features the 'Agency Shared Knowledge' logo and the title 'SDC Projects'. A left-hand navigation menu includes 'Home', 'Documents', 'All General Information', and 'ATG Documents'. The main content area contains several sections: 'Home' with a description of the CTS ASK SharePoint environment; 'Documents' with a description of the site's purpose for managing migrations; 'Other Pages' with links to 'SDC Projects' and 'SDC Migration Calendar'; and 'UPDATES' with a recent update dated 3/19 regarding a customer kick-off meeting. A search box is located in the top right corner. A photograph of a server room is also visible on the right side of the page.

**Note: Site access is provided to current migration customers.**

# Q&A



The IT partner of choice for agencies in Washington state

# Next Meeting

Our next meeting will be **December 17<sup>th</sup>** 2:00 – 3:00 p.m. in **Room 2320**

**This is a change from our typical fourth Thursday schedule and room!**

All meetings will be held at [1500 Jefferson Building](#).

Our online [Meeting Calendar](#) is continually updated with meeting materials.

# Contact Information

- Doug Wood – WaTech Project Manager  
[Doug.Wood@watech.wa.gov](mailto:Doug.Wood@watech.wa.gov) 360.407.8631
- Senthil Masilamani – WaTech Project Manager  
[Senthil.Masilamani@watech.wa.gov](mailto:Senthil.Masilamani@watech.wa.gov) 360.407.8635
- Heidi Brownell – WaTech Chief Project and Planning Officer  
[Heidi.Brownell@watech.wa.gov](mailto:Heidi.Brownell@watech.wa.gov) 360.407.8980
