

State Data Center Agency Implementation Coordinator Meeting

December 17th, 2015

2:00 – 3:00 p.m.

Attendees: SDC Project Staff and Agency Implementation Coordinators

Time	Topic	Presenter
2:00 – 2:10	Welcome & Introductions	All
2:10 – 2:35	Update on SDC Projects	Heidi Brownell
2:35 – 3:00	Q&A	All
3:00 p.m.	Adjourn	

Additional Instructions:

- **Meeting Location -** 1500 Jefferson Building [[PDF Map](#) or [Mapped with Google](#)]
Conference Room 2320

State Data Center (SDC)
*Agency Implementation Coordinator
Meeting*


December 17, 2015

Agenda

- Welcome – Introductions/Review Agenda
- Update on SDC Projects
- Customer Communications
- Q&A

SDC Projects

SDC Projects Timeline

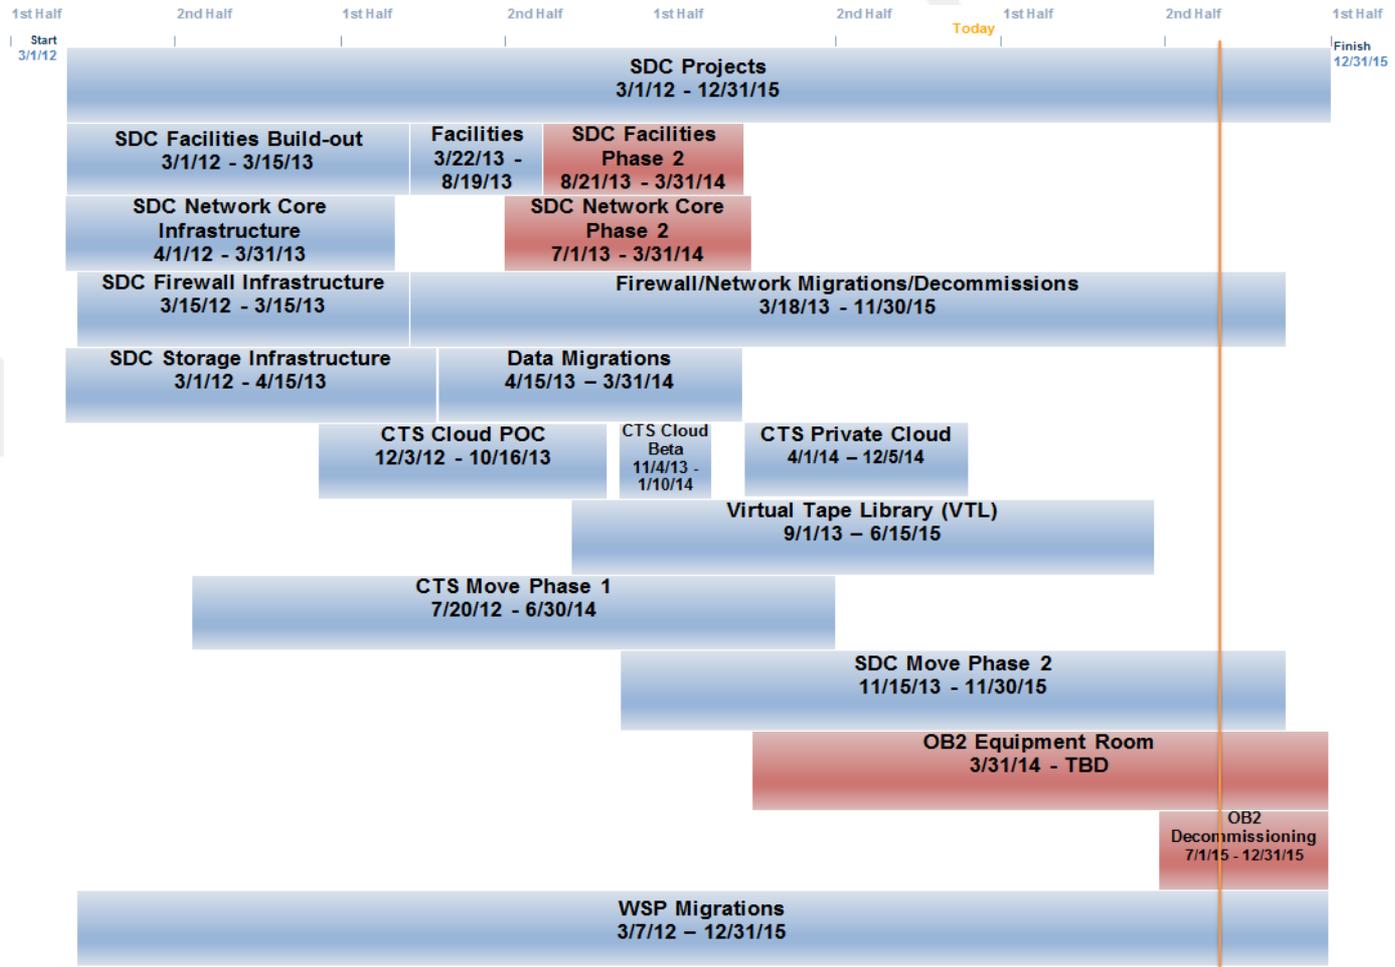

The IT partner of choice for agencies in Washington state

SDC Firewall Project

Firewall Migrations

Recent:

- Decommissioned remaining four firewalls


Upcoming:

- Project Complete!

Firewall Migrations

CTS Firewall Migration / Decommission Schedule

As of 12/17/2015

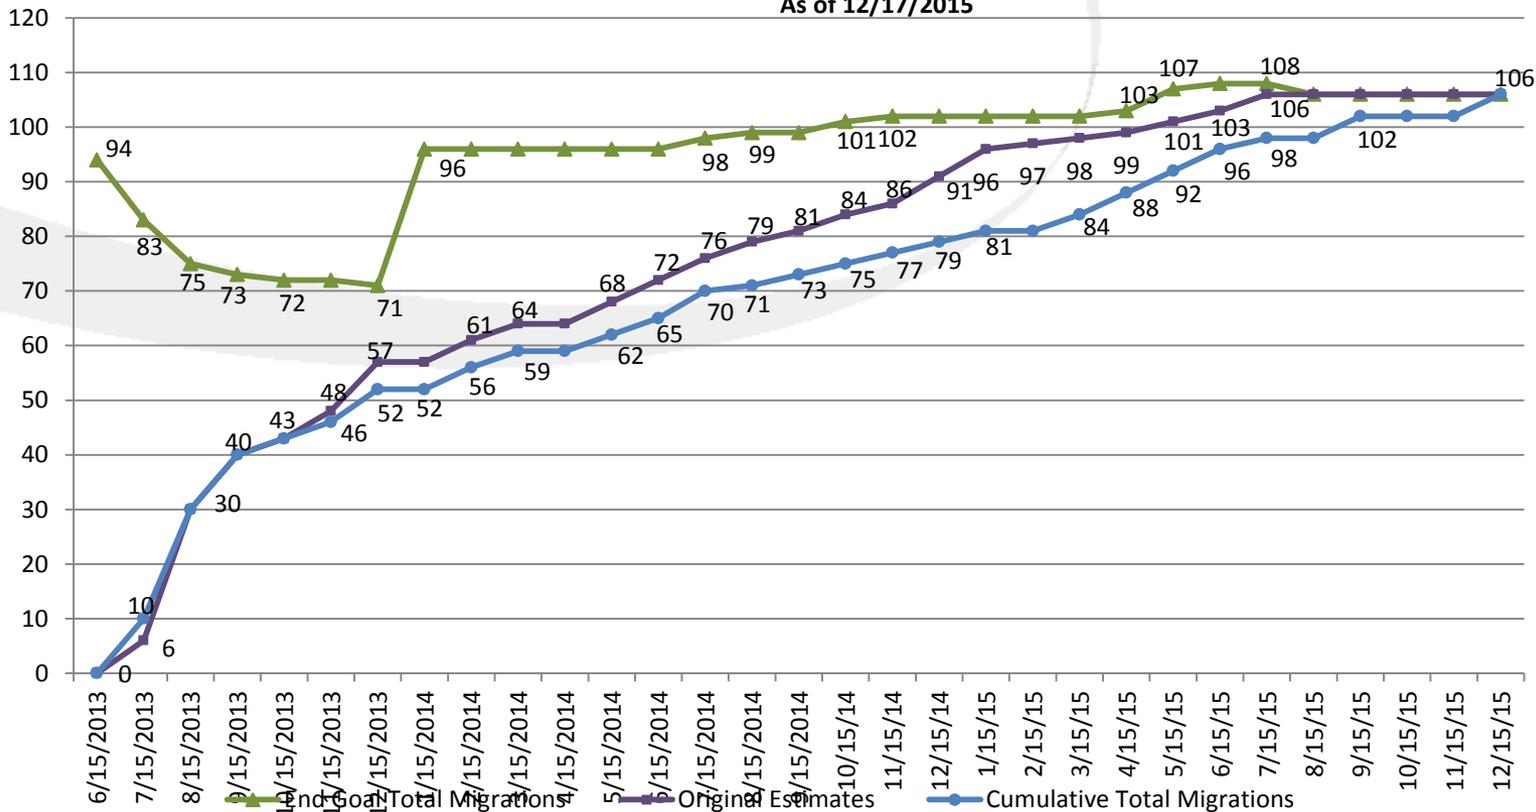

SDC Move Phase 2

SDC Move Ph 2- CTS Devices

Recent:

- No activities performed

Upcoming:

- Decommission enclosures that are remaining in OB2 to support DES Print

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

SDC Move Ph 2- Security

IPSEC Site-to-Site/Branch Office

Recent:

- Migrated VPN concentrator to SDC on Nov 18th
- Transferred final migrations to OPs team

Upcoming:

- Project Complete!

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

SDC Move Ph 2– Network

Migrate Access Layer and 6509s to SDC

Recent:

- Completed 30 migrations

Upcoming:

- Perform final migrations (must wait for PRINT)

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

Total # Remaining

23

Total # Connections

716



WSP

The IT partner of choice for agencies in Washington state

WSP

Recent:

- Conducted network and SDC Facility consults to support upcoming onboarding events
- Performed cabling requests to support circuit installations in the SDC

Upcoming:

- Final hardware install delayed to January
- Close-out project on WaTech side, but continue to support WSP projects/operations

SDC Move Phase 2

CTS Devices

Security

Telephony

Network

Customer Migrations

OB2 Equipment Rm

OB2 Equipment Room

DES, WaTech, and DSHS have been meeting to discuss the requirements, plan, and design of the future state of vacated data center space in OB2. Some Telephony and LAN equipment will need to stay in OB2 to support the tenants.

Recent:

- Met with new DES contact regarding open items
- Scheduled meeting for January

Upcoming:

- Continue supporting DES as requested

OB2 Decommissioning

Vendor Trunk Migrations

Recent:

- Vendor performed re-work on a circuit extension
- Completed legal review and procurement to support move of the remaining trunk

Upcoming:

- Perform circuit cutover once extension rework is completed
- Schedule final move (one trunk, four circuits) with vendor and impacted customers

Total # Remaining	4
Total # Circuits	335

Campus Fiber Network

Recent:

- Performed DOT, DNR, LSC, LTS, MIL & SAO circuit migrations

Upcoming:

- Perform DES circuit migration
- Perform circuit analysis on T0026S-144
- Schedule P130S & P333S fiber trunk migrations with vendor


Total # Remaining

216

Total # Connections

720

Campus Fiber Network Activity Pipeline

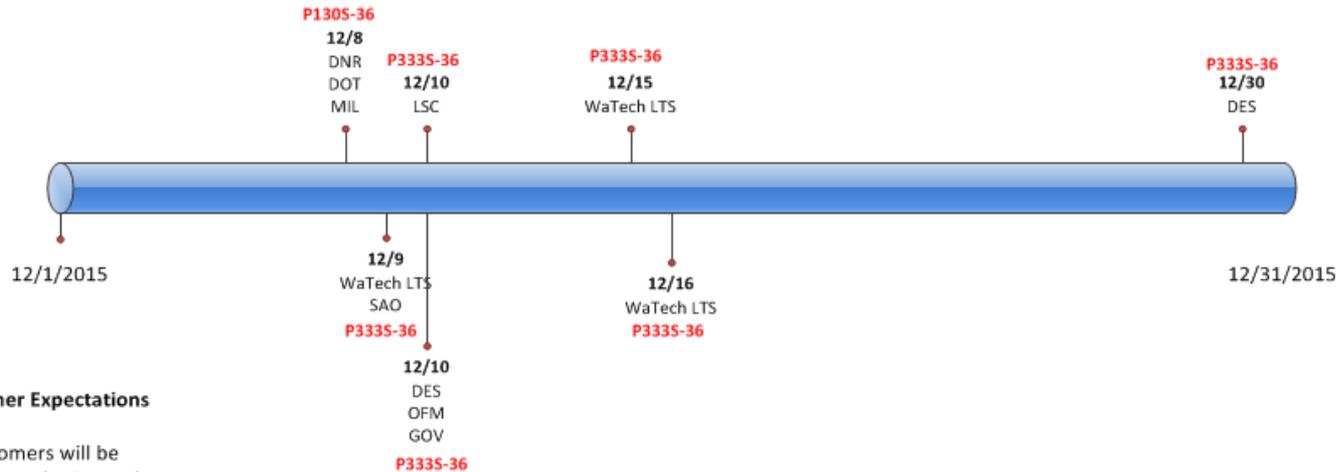

Customer Expectations

- Customers will be contacted prior to the target move date to set the schedule.
- Customer approves schedule, establishes test scenarios, performance benchmarks and prepares for move.
- Customer Coordination continues through entire move cycle.
- Customer gives final acceptance of move completion.

December 2015 CFN Migrations		
Dec 8 P1305-36 <ul style="list-style-type: none"> • DNR • DOT • MIL 	Dec 9 P3335-36 <ul style="list-style-type: none"> • SAO 	Dec 10 P3335-36 <ul style="list-style-type: none"> • DES • GOV • OFM
Dec 15 P3335-36 <ul style="list-style-type: none"> • WaTech LTS 	Dec 16 P3335-36 <ul style="list-style-type: none"> • LSC 	Dec 30 P3335-36 <ul style="list-style-type: none"> • DES

Pending Scheduling	
TBD 2016	
T00265-144	
<ul style="list-style-type: none"> • COMCAST • CTS • DES • DOL • DOT 	<ul style="list-style-type: none"> • DSHS • SAO • SOS • WaTech LTS

OB2 SMON Node Relocation

This project will move customer connections in the OB2 Node to another node.

Recent:

- Completed LEG SMON Node Reconfiguration and Equipment Removal

Upcoming:

- Reschedule DOL SGN Migration

Total # Remaining

2

Total # Connections

18

Move Telephony Equipment

Recent:

- Continued work to consolidate and decommission enclosures

Upcoming:

- Continue consolidating and decommissioning enclosures
- Work with DSHS and DES to move to the equipment room

Customer Communications

SDC Project Website

AIC Meeting Wrap-Up:

The [SDC Projects](#) website will continue to provide current information about the status of the projects until all activity is complete.

The screenshot shows the SDC Project Website interface. At the top left is the CTS logo and a quote: "CTS' Exchange 2010 environment called out as one of the best evaluated! Read more". A search bar is on the top right. The navigation menu includes Home, Products and Services, and Projects. Below the menu, the breadcrumb trail reads "Home > Projects > State Data Center". The main content area is titled "State Data Center Projects" and features a news item dated "April 30, 2014" about "SDC Move Phase 2". The news item describes customer migration kick-off meetings and lists high-level accomplishments for "CTS Move Phase 1", such as Fortress Customer Test and Production migration, telephony migrations, and server decommissioning. It also mentions "Network and Firewalls" migration and "Facilities/Network Core Phase 2" readiness. An "Important Links" sidebar on the right lists Home, Customer Readiness, Background, Status Report Archive, Meetings, Migration Calendar, and Archived Updates. At the bottom, there are two summary boxes: "BUDGET: SDC Projects Spending Plan" with a bar chart titled "SDC Projects Lifecycle Budgets and Actuals" and a note that the chart shows baseline budget and actuals for all SDC projects; and "STATUS: Current Status Report" with a table showing the status of various SDC projects.

SDC Projects	Scope	Sched	Budget
SDC Program	●	●	●
OB2 Heat Reduction		(completed)	
SDC Facilities		(completed)	
SDC Network Core		(completed)	

Migration Calendar Updates

Customers on the SGN can view migration events on the [SDC Migration Calendar](#).

SDC Migration Calendar

CTS began migrating equipment and systems from the existing data center (OB2) to the State Data Center (SDC) in December 2012. Migrations will continue for many months. CTS currently publishes [Technical Bulletins](#) to notify customers of upcoming changes.

Important Links

- [State Data Center projects](#)
- [Customer Readiness](#)
- [Background](#)
- [Status Report Archive](#)
- [Meetings](#)
- [Migration Calendar](#)
- [Archived Updates](#)

December 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1)	2)	3)	4)	5)
6)	7)	8) Campus Fiber Network Migration: DOT, MIL, DNR	9) Campus Fiber Network Migration: SAO	10) Campus Fiber Network Migration: DES, OFM, GOV	11)	12) SDC Projects: SAO SDC Onboarding
13)	14)	15)	16) Campus Fiber Network Migration: LSC	17)	18)	19)
20)	21)	22)	23)	24)	25)	26)
27)	28)	29)	30)	31)		

Migration events in green font denote an internal CTS test system migration with no customer impact. A Technical Bulletin will not be issued for these events.

Next Meeting

Meetings complete!

Q&A



Feel free to contact Heidi Brownell with any questions.

Heidi.Brownell@watech.wa.gov 360.407.8980
