



Consolidated Technology Services • WA

Agenda

SDC Projects Steering Committee

October 3, 2012
1:00 pm to 2:00 pm
Conference Room 2208

- SDC Projects Reports – Service Owners
- SDC Roadmap
- Project Milestone Report
- Top Issues

Next Meeting: October 17, 2012



Consolidated Technology Services • WA

Meeting Minutes

**State Data Center Projects
Steering Committee
October 3, 2012
1500 Jefferson, Rm 5092**

Steering Committee Attendees: Christy Ridout, Dan Mercer, Gordon Ice, Dan Davis, Wendy Huff, Heidi Brownell, Doug Hieronymus, Aaron Robel, Phil Davis, Bruce Shurtz

Not present: Agnes Kirk, Lance Calisch, Debbie Kendall, Bob Walk, Kay Metsker

Other Attendees: Rick Cook, Sally Alhadeff, Scott Lindekekugel, Michael Breton

ISSUES AND/OR DISCUSSION	
Agenda Topic	Discussion
SDC Projects Reports	<p>SDC Program:</p> <ul style="list-style-type: none"> A cross-divisional team is meeting to identify lab requirements. Due to heavy resource focus on NWC, Facilities readiness, etc the lab readiness will likely be Feb 1. The Operational Model and SLA drafts are being targeted for a November Steering Committee review. <p>Heat Reduction:</p> <ul style="list-style-type: none"> The heat reduction project is on track to complete at the end of this month. <p>Facilities:</p> <ul style="list-style-type: none"> The team is supporting the NWC Rack and Stack this week. Antennea are going in on the roof. The timing generator is next week. Doug will send the SDC draft procedures to Heidi so they can be posted on the SharePoint site. We will review them at Steering Committee. <p>NWC:</p> <ul style="list-style-type: none"> The team is currently working on the rack and stack. 12/8 is still the date for NWC readiness. <p>Firewall:</p> <ul style="list-style-type: none"> Lab gear should be here today or tomorrow. Oct 15th the Fortinet contractors will be onsite. <p>Storage:</p> <ul style="list-style-type: none"> The team is still working through the contract and SOW with the intent to finish both together. They are meeting daily now. Working with network folks to complete purchase requests for the remaining storage gear. Gordon will schedule a pre-brief with Christy and Rob so that approval occurs as quickly as possible. <p>OB2 Ph1:</p> <ul style="list-style-type: none"> The Investment Plan is being finalized. Hardware planning sessions with security have kicked off and the team is working on dependency mapping



ISSUES AND/OR DISCUSSION	
Agenda Topic	Discussion
	<ul style="list-style-type: none"> Working on sequencing server moves based on necessary refresh timeframes, customer demands, and resource constraints. WSP: <ul style="list-style-type: none"> Completed the detailed network design and enclosure design. Drafted Interagency Agreement.
SDC Roadmap	<ul style="list-style-type: none"> The team has been developing the SDC Roadmap. Dan passed around a document that defines the scope of the work for the workgroup to ultimately create a Roadmap. The team shared a high level overview of their work to date.
Milestone Report	(Reviewed as part of above projects updates above)
Top Issues	<ul style="list-style-type: none"> Several issues were closed recently. Service Owners need to be sure that their projects' issues are entered into the issue log.

The [meeting presentation](#) can be found on the project's [SharePoint](#) site.

1. New Action Items

Item	Action Item	Assignee	Target Due Date	Comments
1	Doug will send the SDC draft procedures to Heidi so they can be posted on the SharePoint site. We will review them at Steering Committee.	Doug	10/4/2012	
2	Gordon will schedule a Pre-brief with Christy and Rob.	Gordon	10/10/12	


2. Upcoming Meetings

Meeting	Details
Next Meeting	October 17, 2012, 1:00-2:00, Room 2208



The SDC Roadmap Effort Update



SDC ROADMAP 2012-201X



SDC ROADMAP 2012-201X

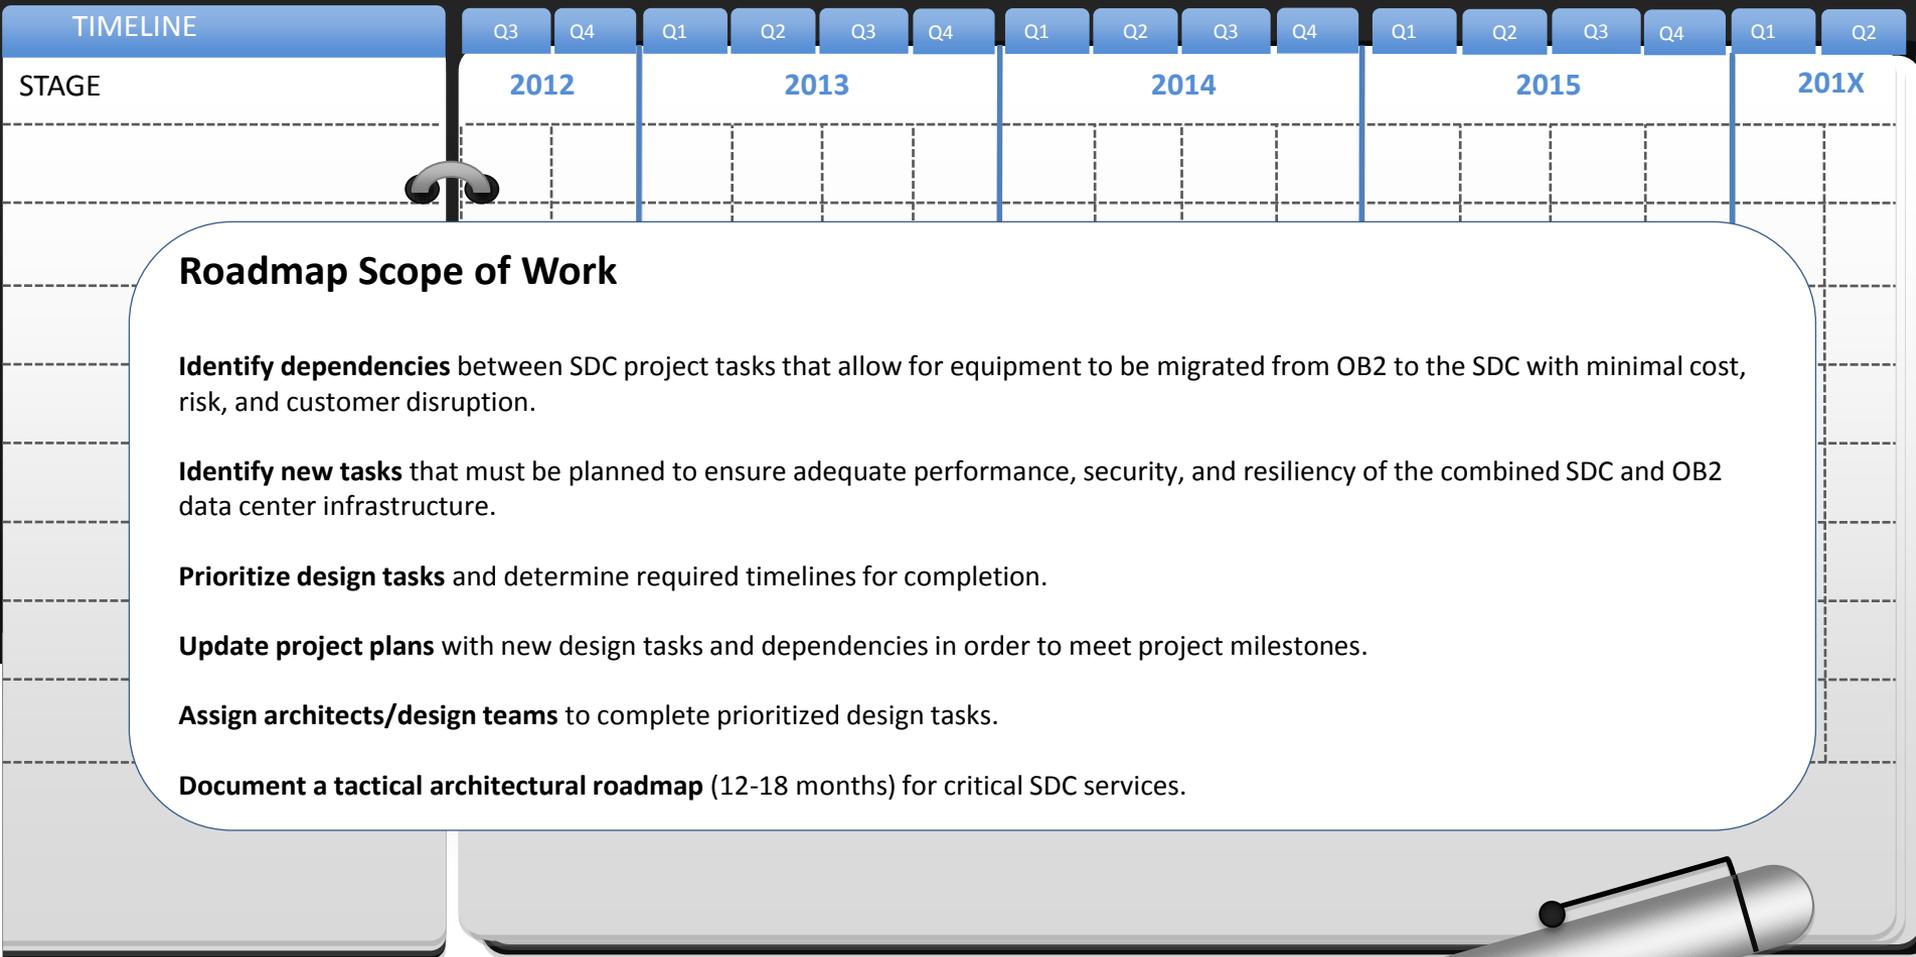

SDC ROADMAP 2012-201X

TIMELINE

Q3

Q4

Q1

Q2

Q3

Q4

Q1

Q2

Q3

Q4

Q1

Q2

Q3

Q4

Q1

Q2

2012

2013

2014


2015

201X


STAGE




SDC ROADMAP 2012-201X

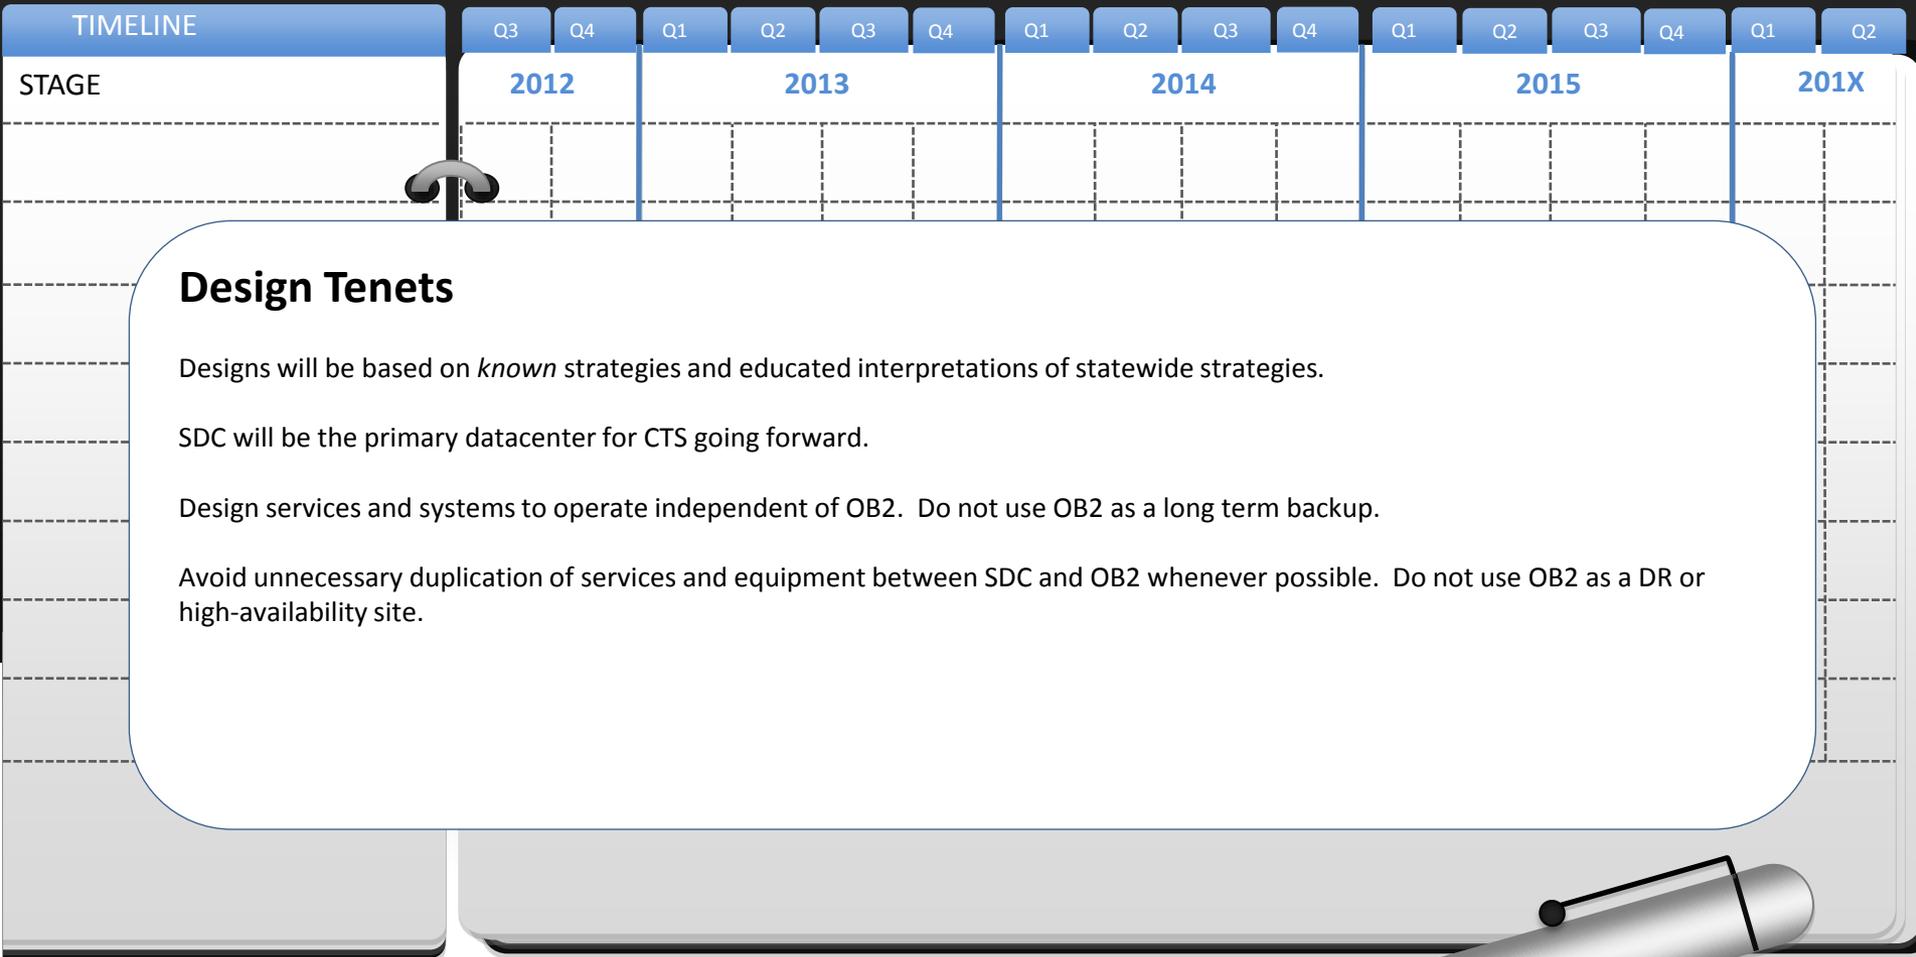

SDC ROADMAP 2012-201X

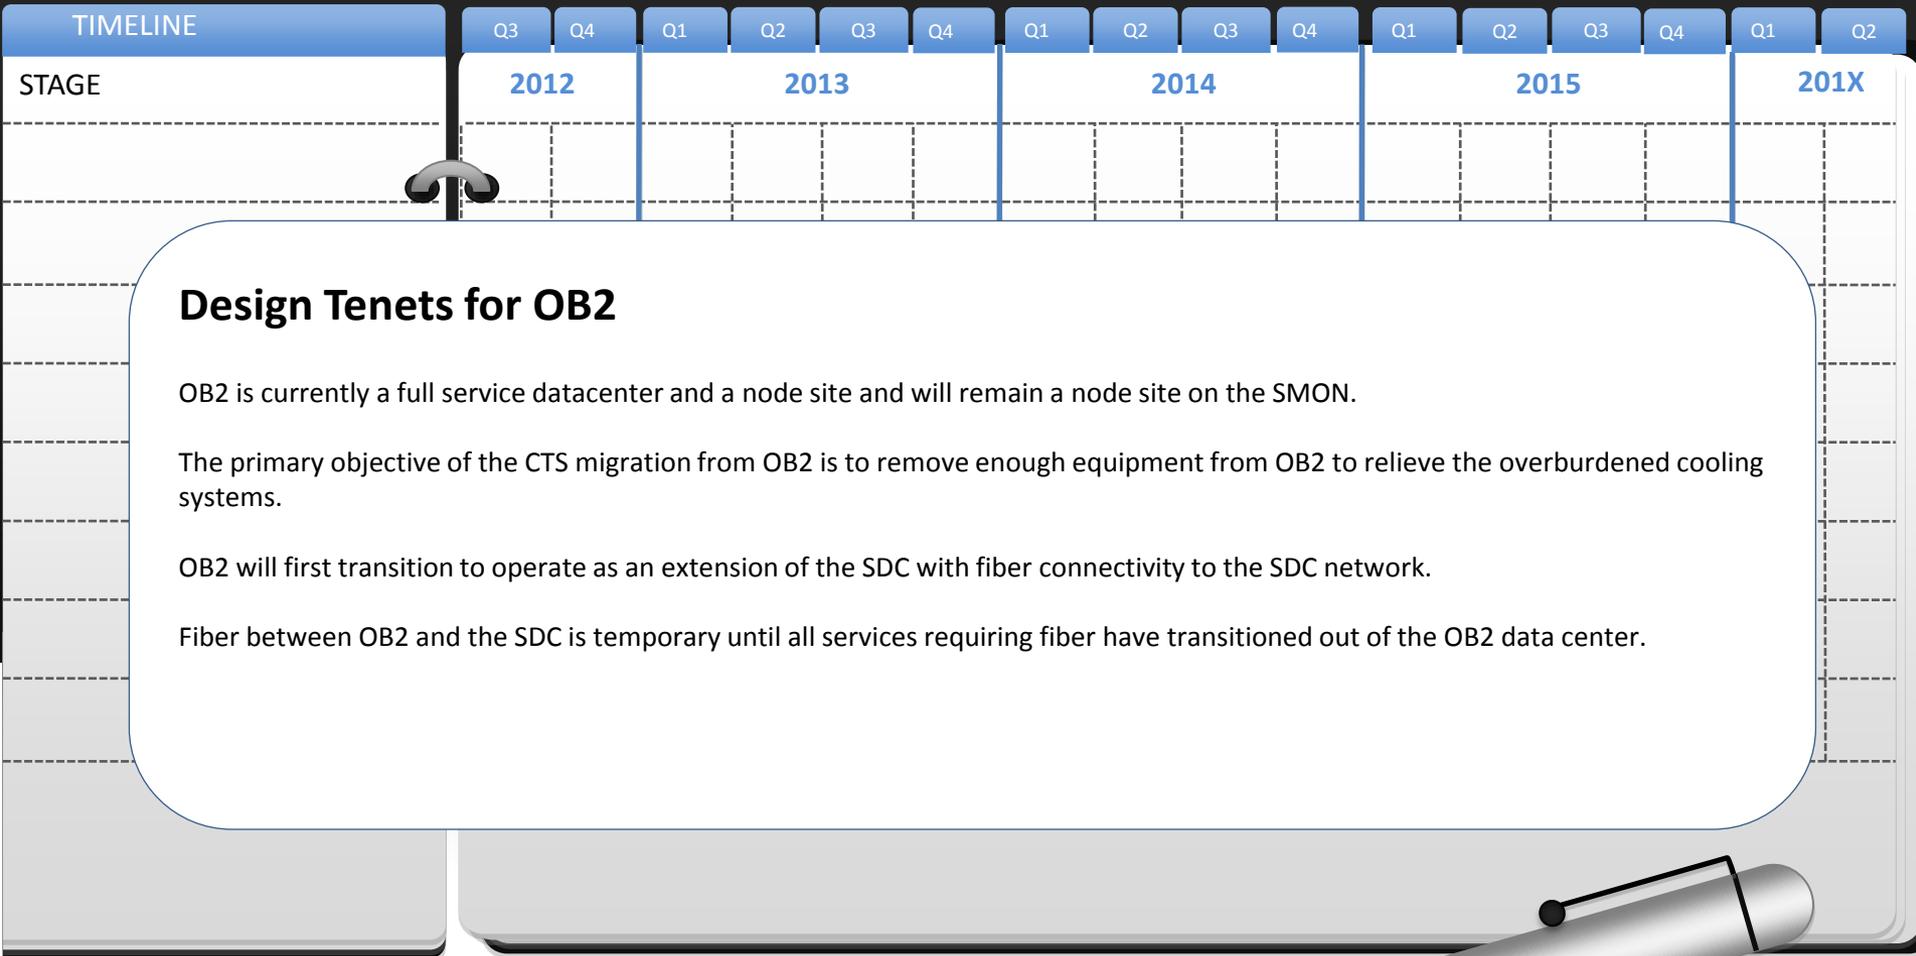

SDC ROADMAP 2012-201X

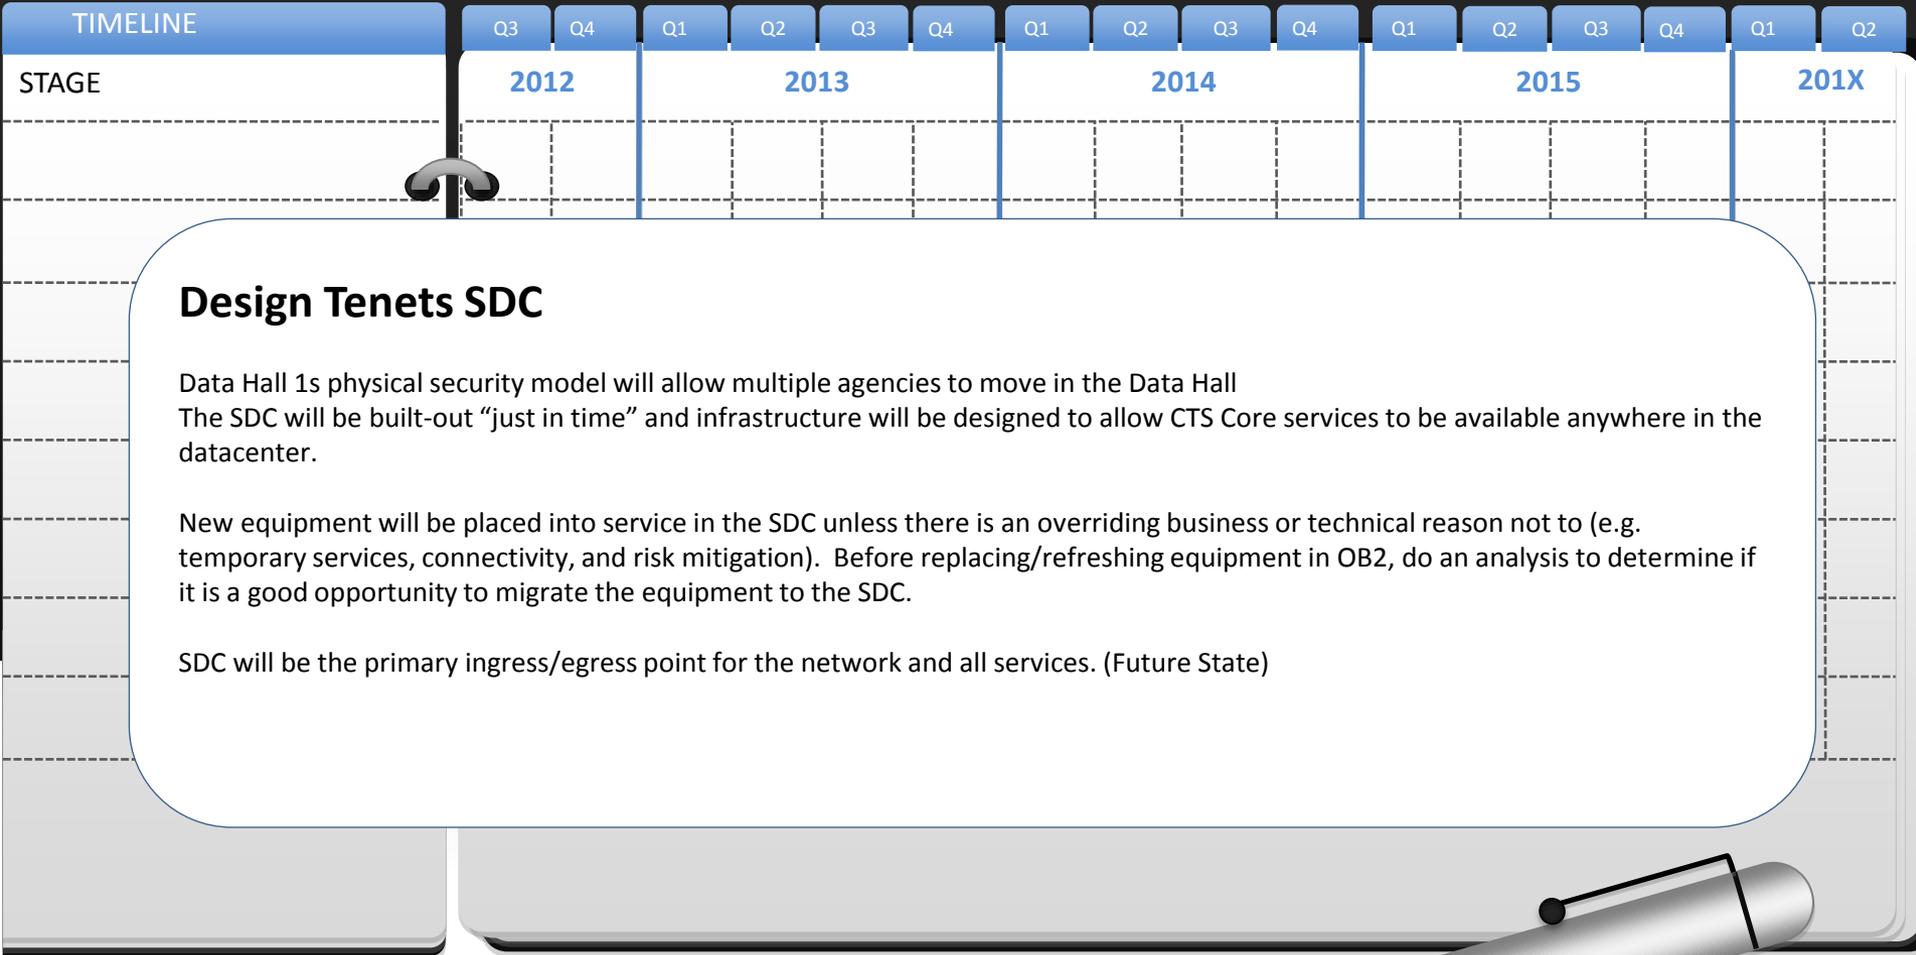


SDC ROADMAP 2012-201X

TIMELINE	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
STAGE	2012		2013				2014				2015				201X	

Two Key Terms


Accessible - The service is not delivered from the SDC, but is reachable via the State Networks

Available - The service is delivered from the SDC and is accessible from all node sites




SDC ROADMAP 2012-201X



TIMELINE	Q3	Q4	Q1	Q2														
STAGE	2012				2013				2014				2015				201X	
Data Hall 1 Available	DH 1																	



SDC ROADMAP 2012-201X

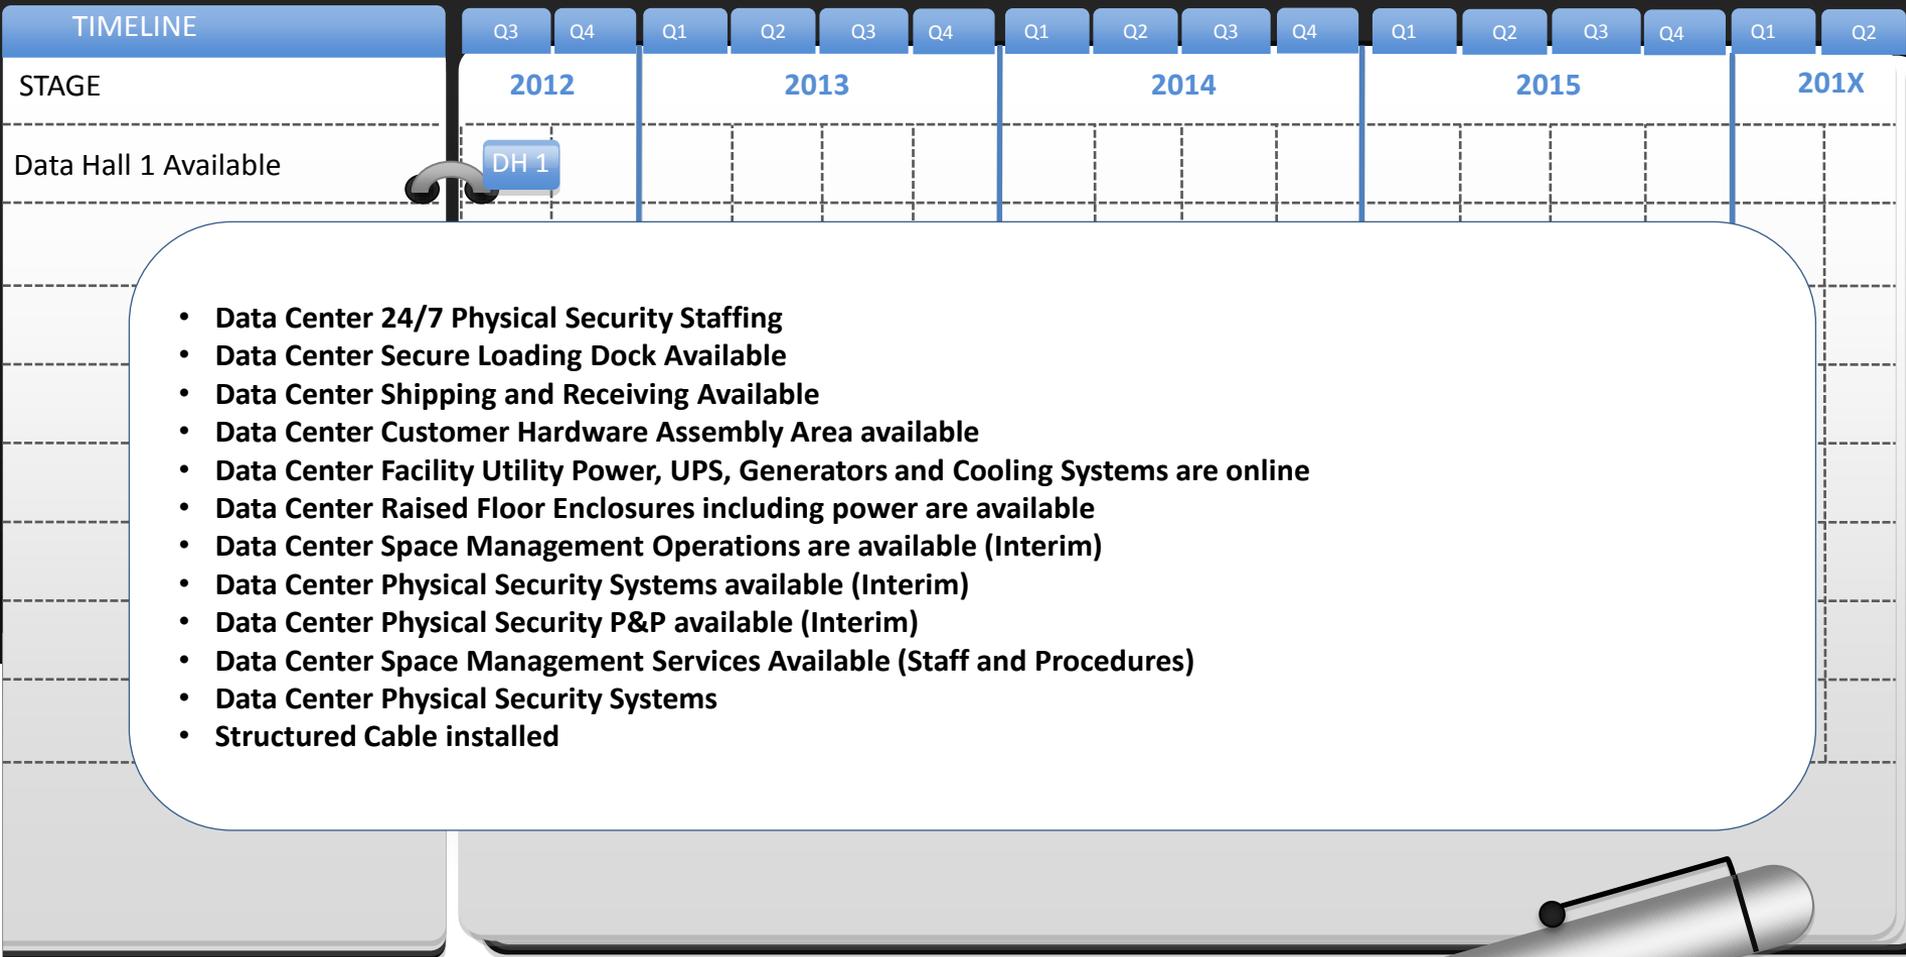


SDC ROADMAP 2012-201X

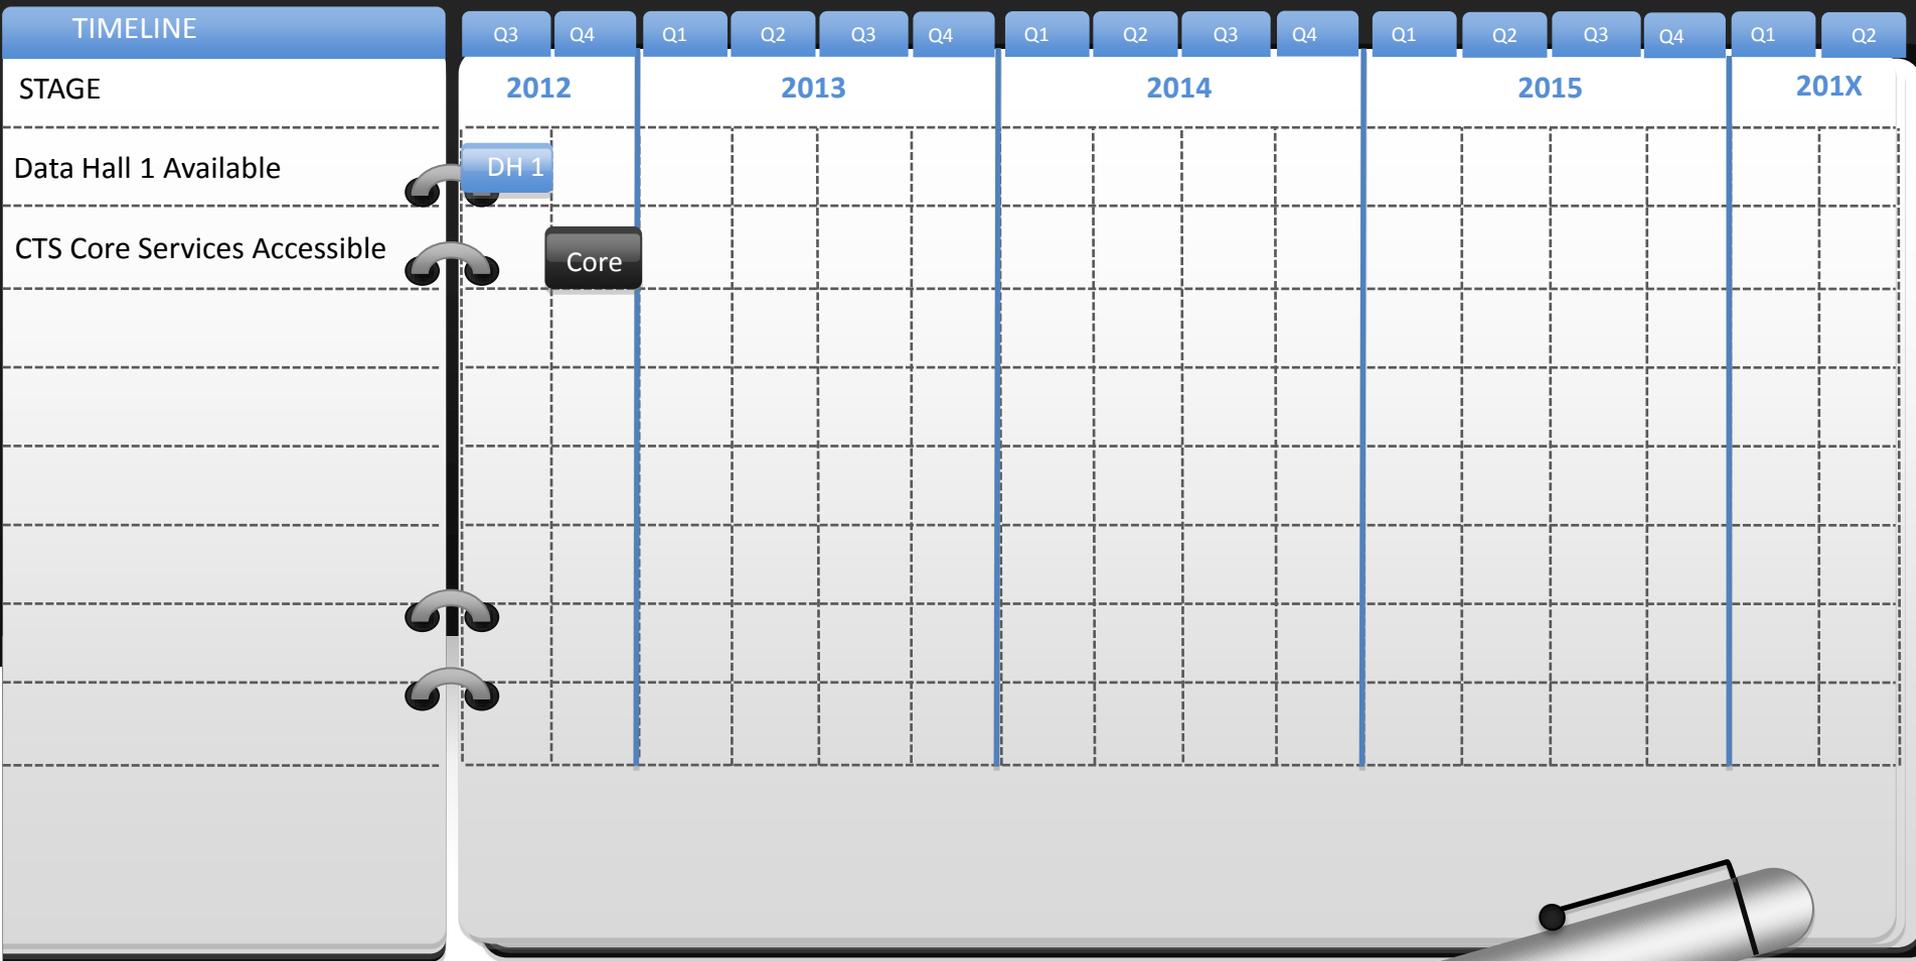


SDC ROADMAP 2012-201X

TIMELINE	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
STAGE	2012		2013				2014				2015				201X	
Data Hall 1 Available	DH 1															
CTS Core S																



- Establishes a single logical data center by connecting OB2 and the SDC into a single extended network
- Fiber connectivity between OB2 East and the SDC is complete
- The Core network is extended between OB2 and the SDC
- SAN fabric extended into the SDC
- Management network installations are complete
- Final Facilities Policies and Procedures for the SDC are published





SDC ROADMAP 2012-201X

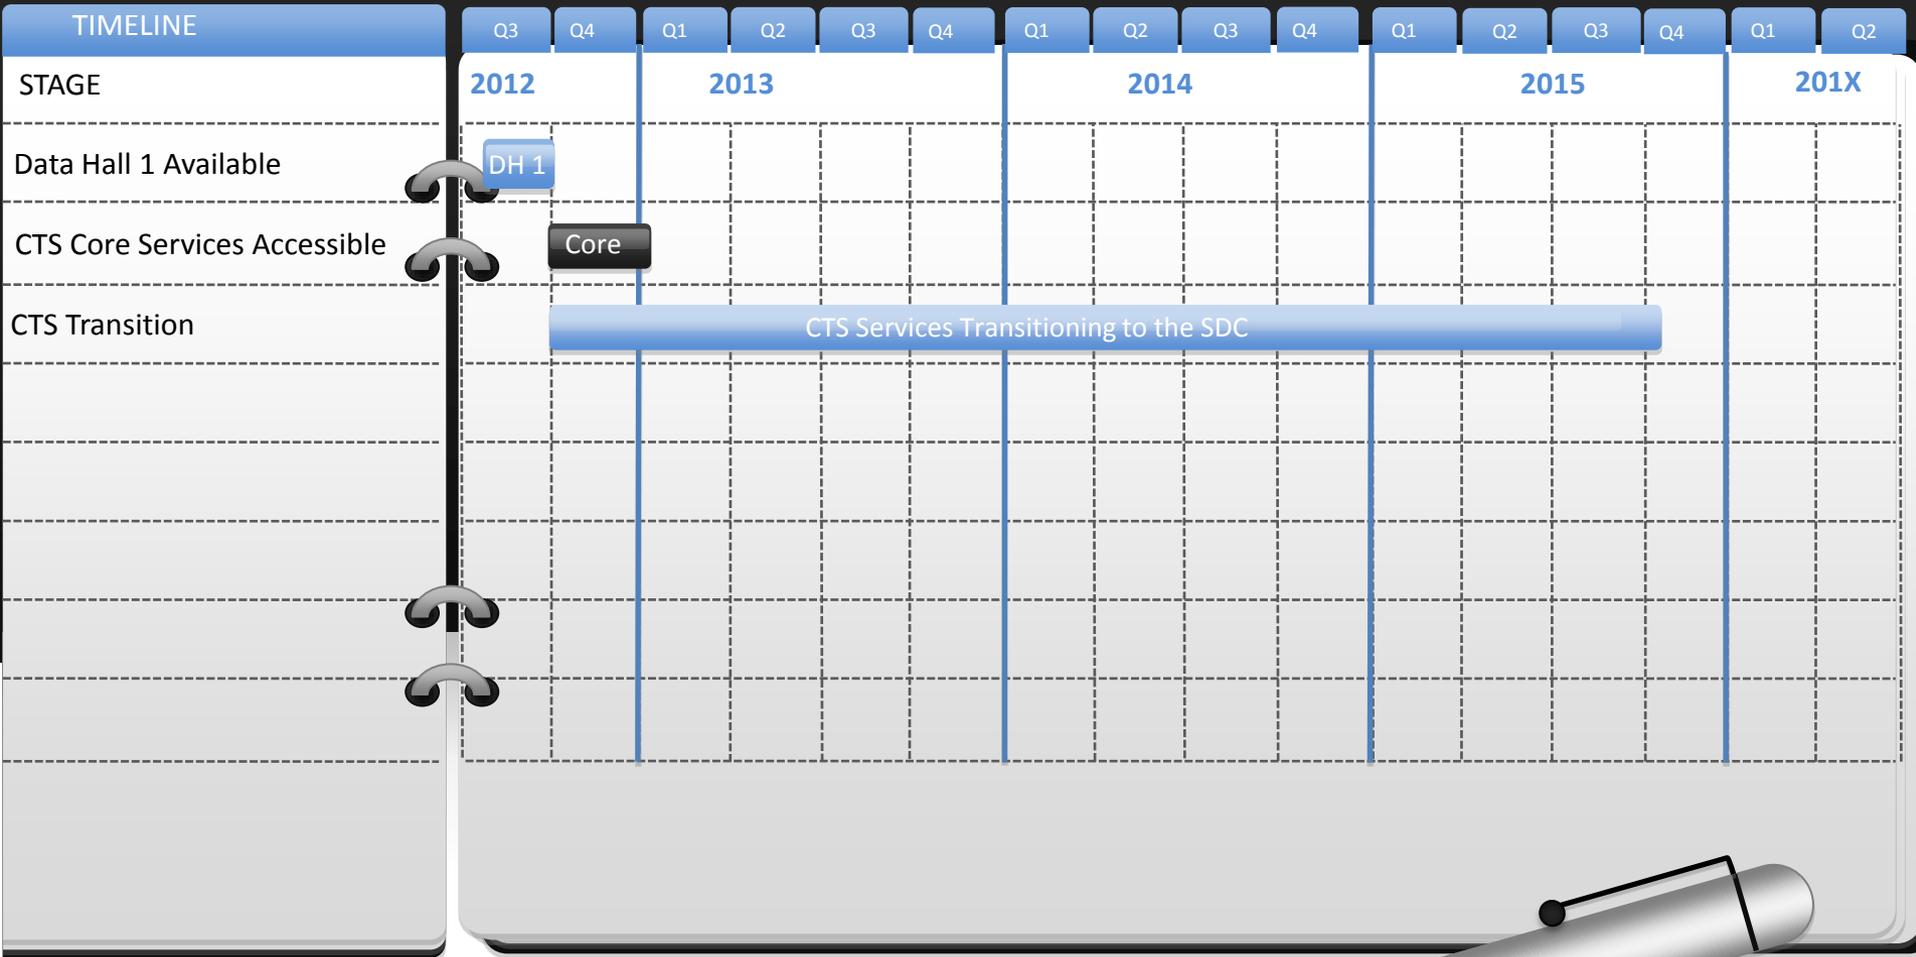


SDC ROADMAP 2012-201X

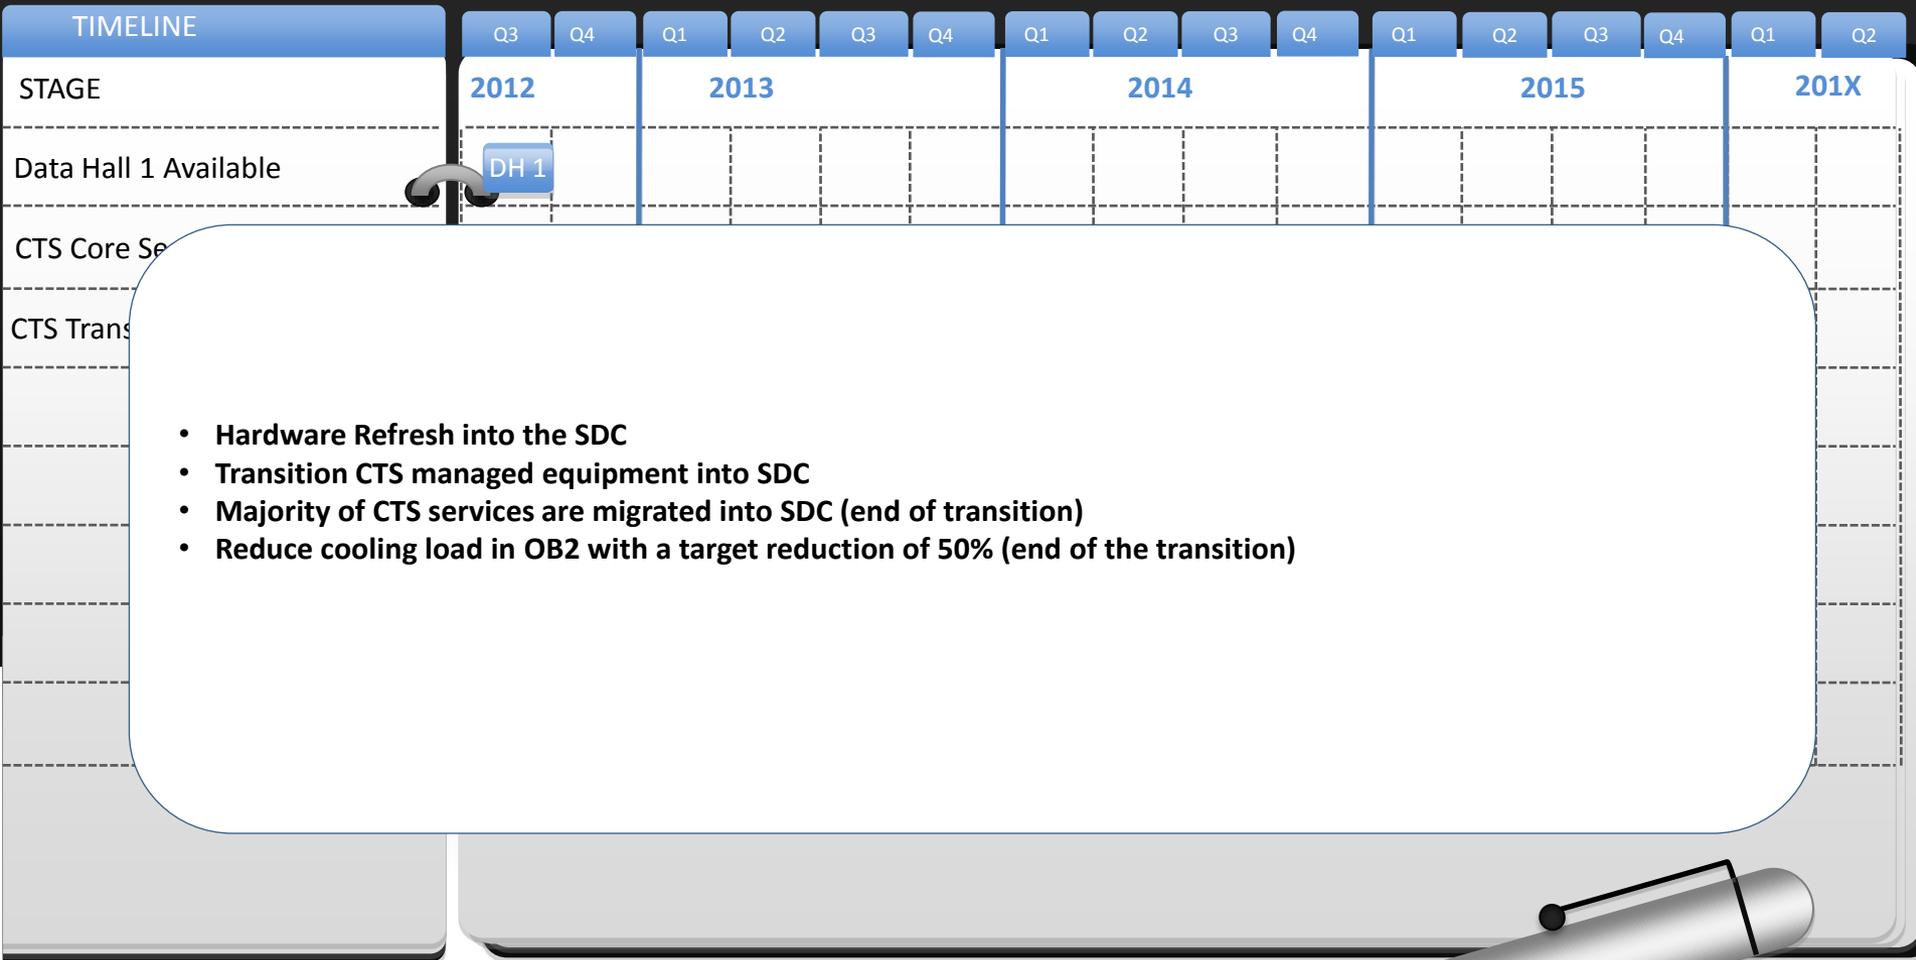



SDC ROADMAP 2012-201X

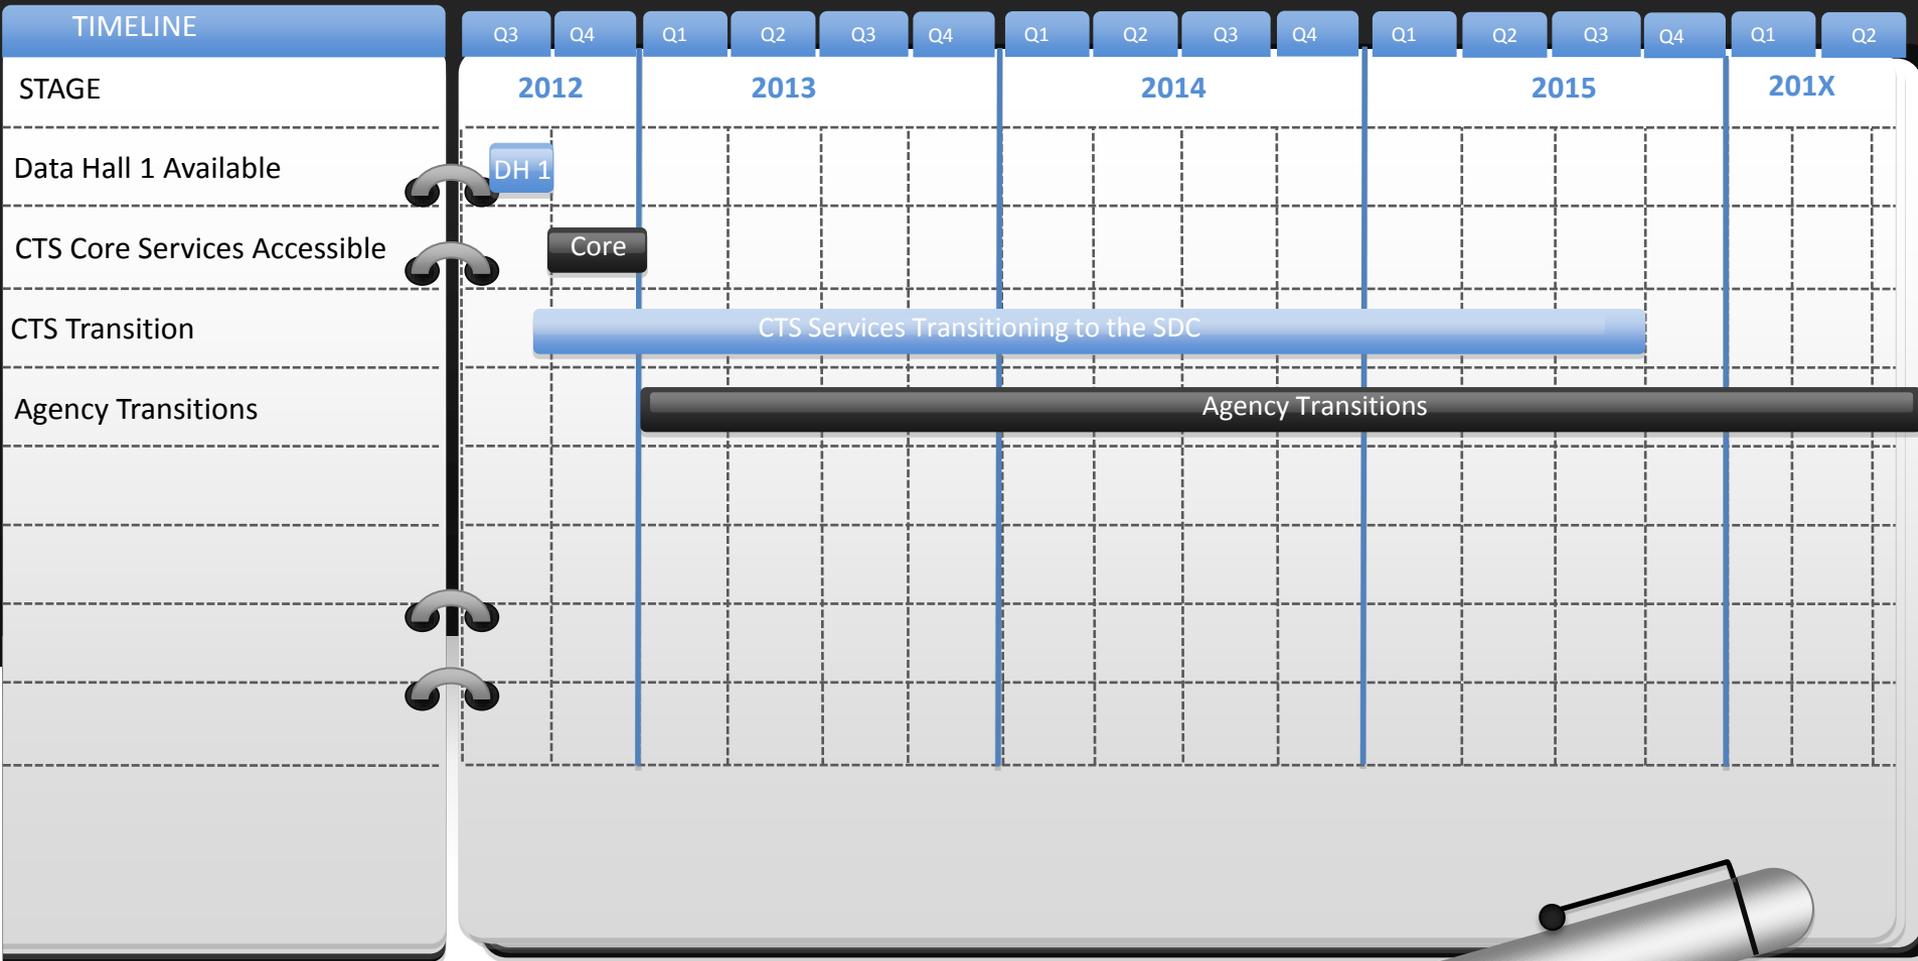



SDC ROADMAP 2012-201X





SDC ROADMAP 2012-201X

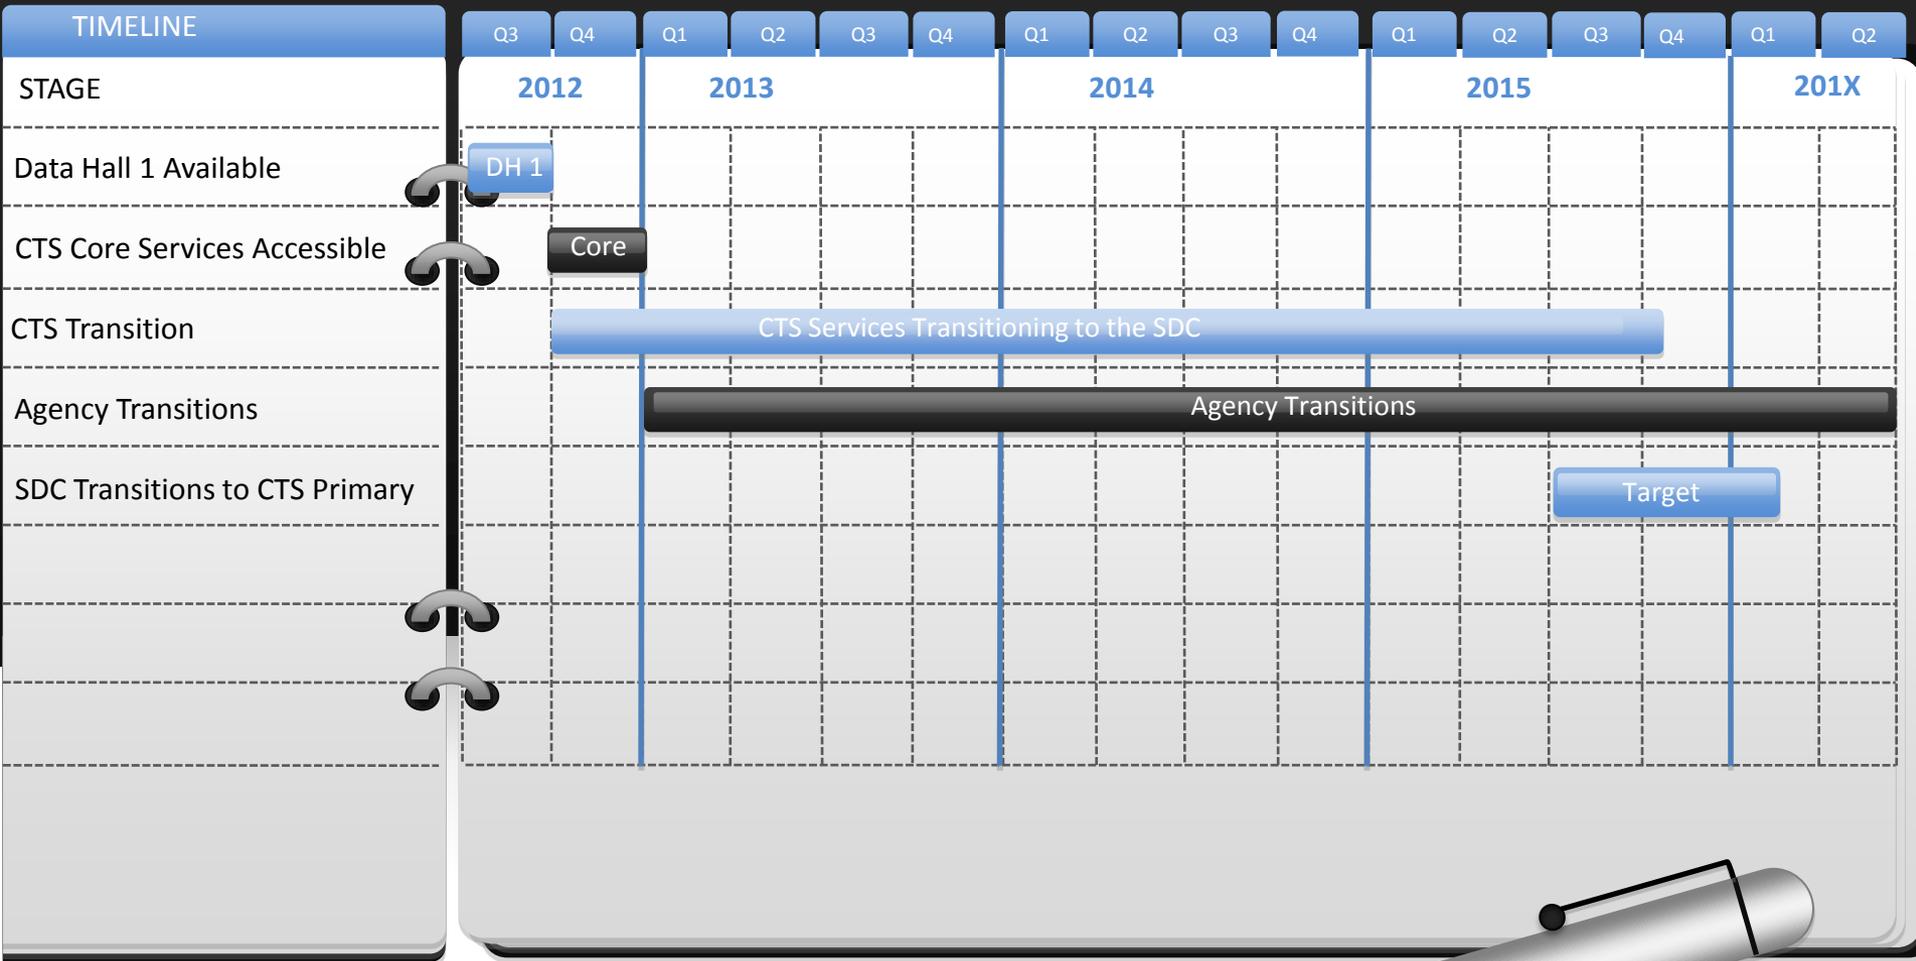



SDC ROADMAP 2012-201X

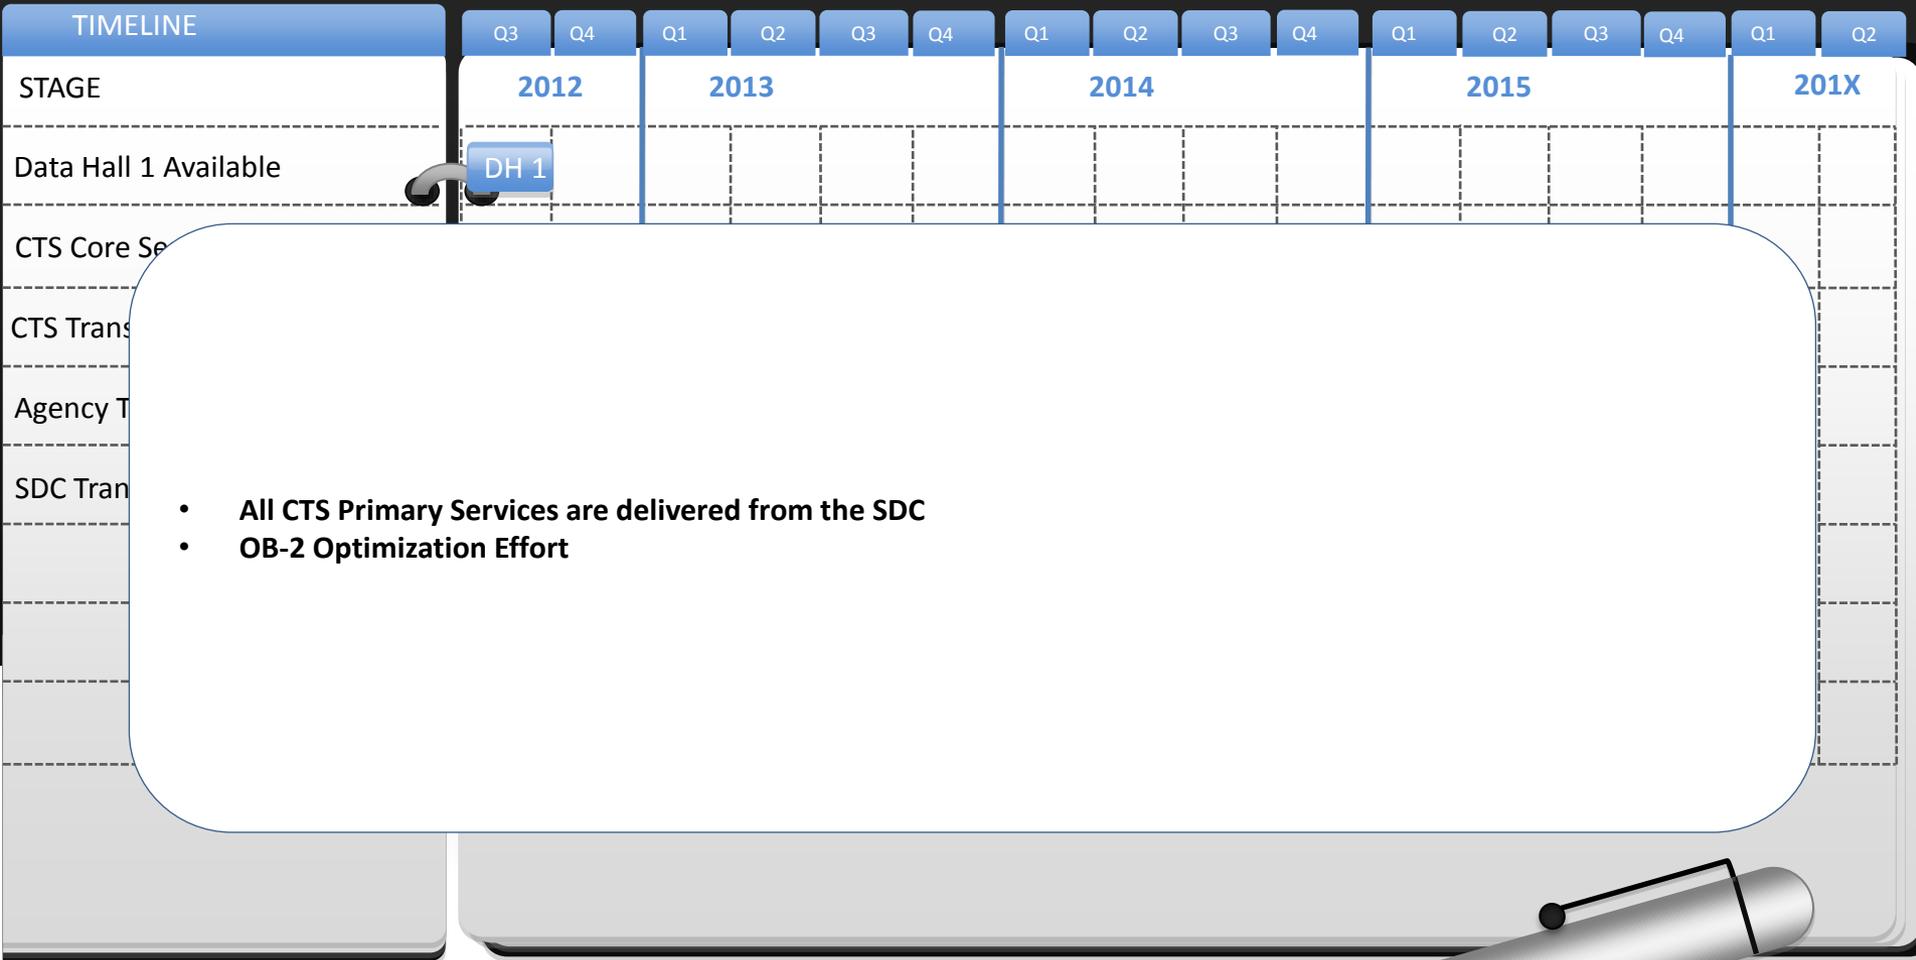



SDC ROADMAP 2012-201X

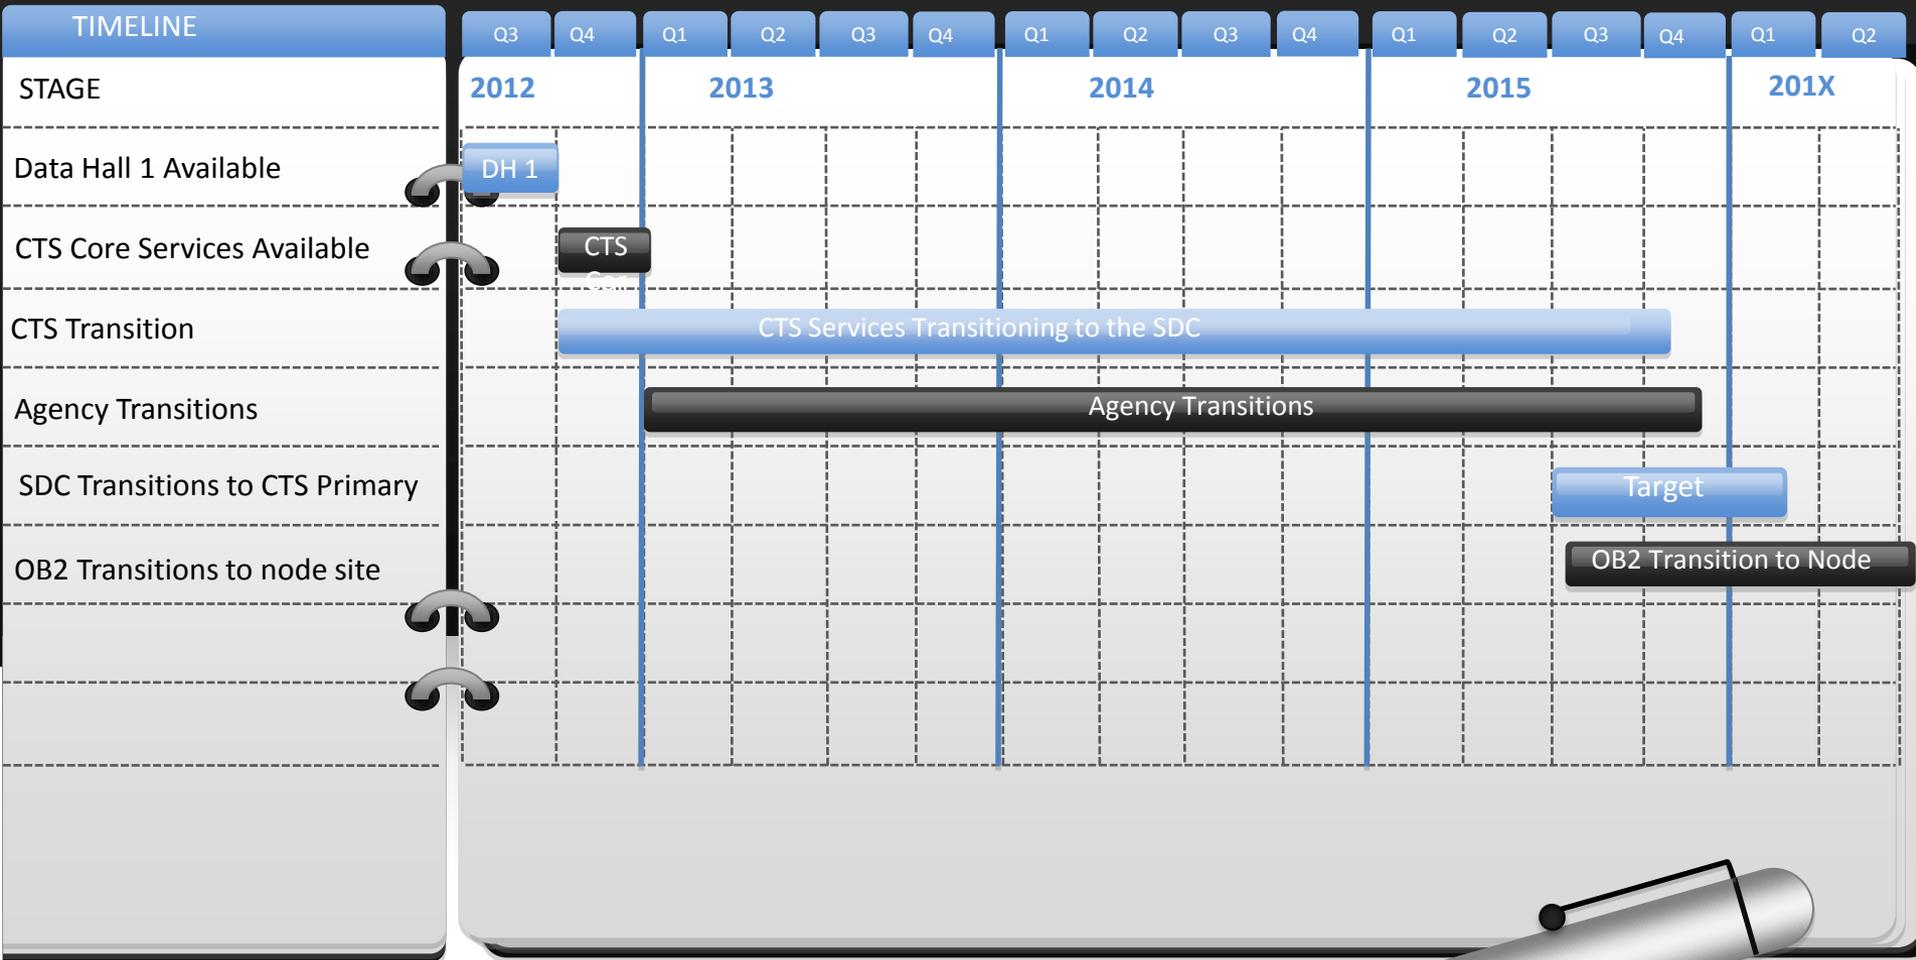


SDC ROADMAP 2012-201X

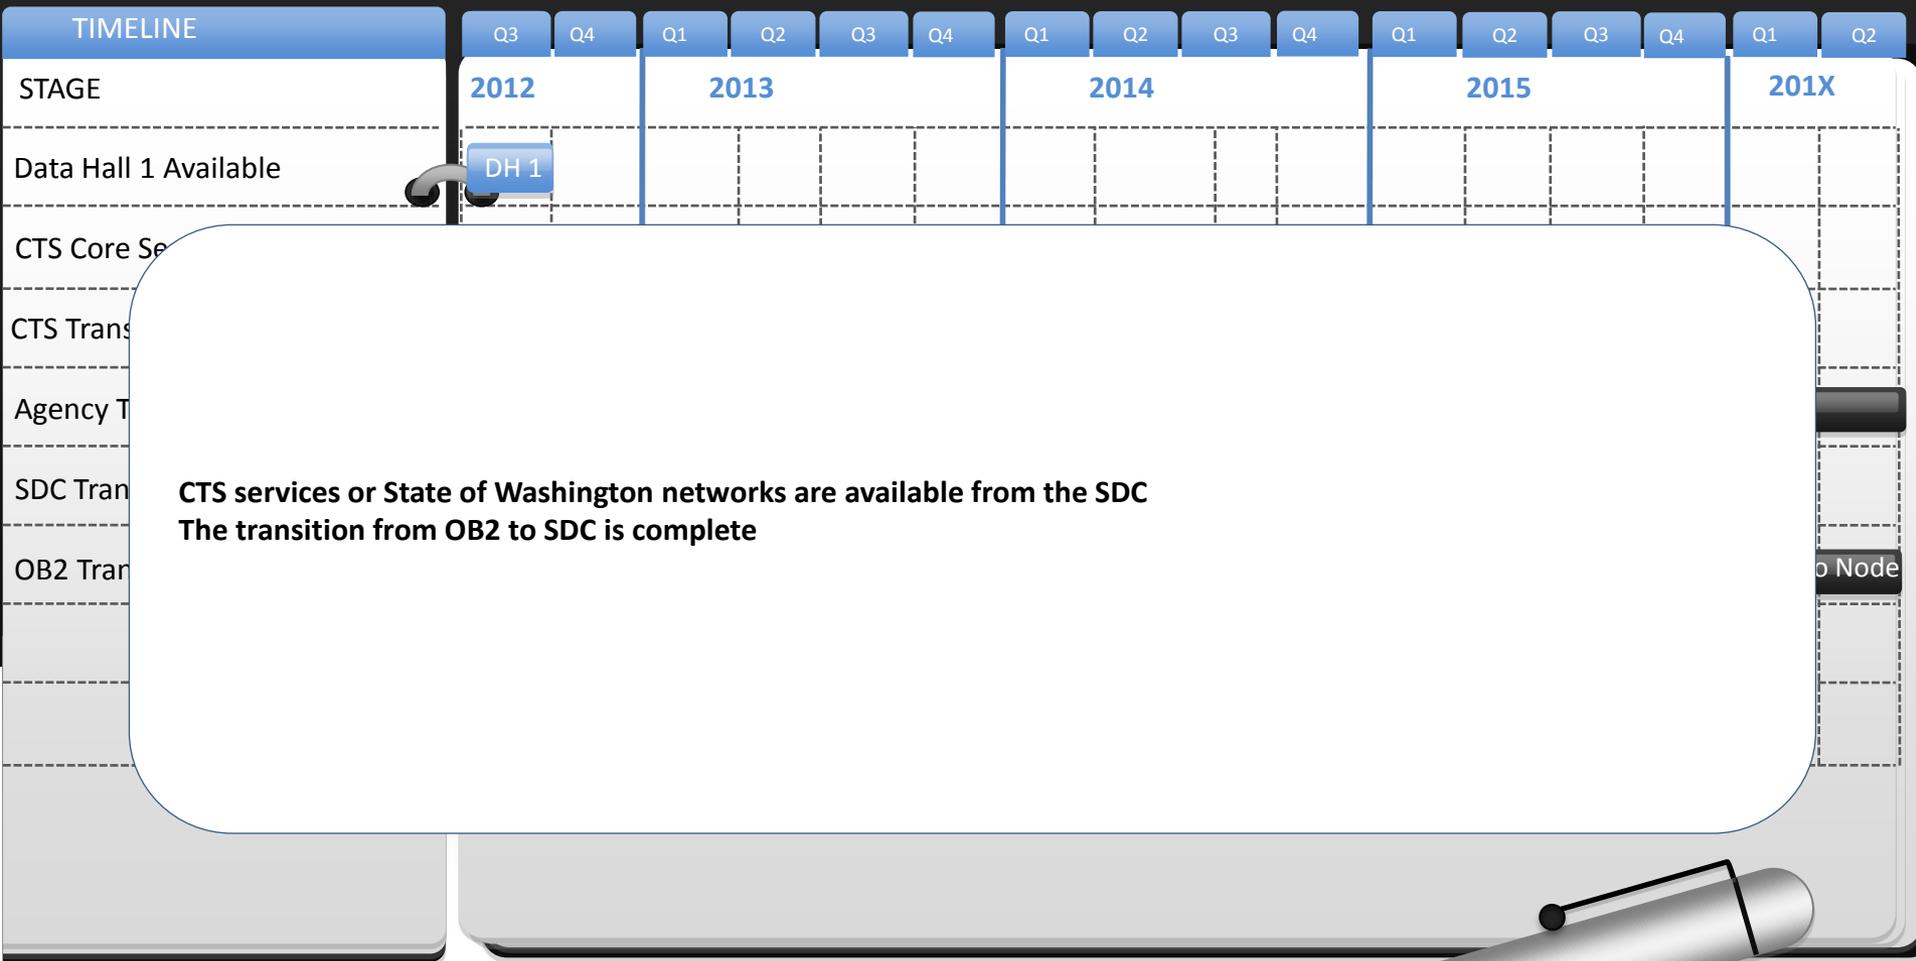

SDC ROADMAP 2012-201X

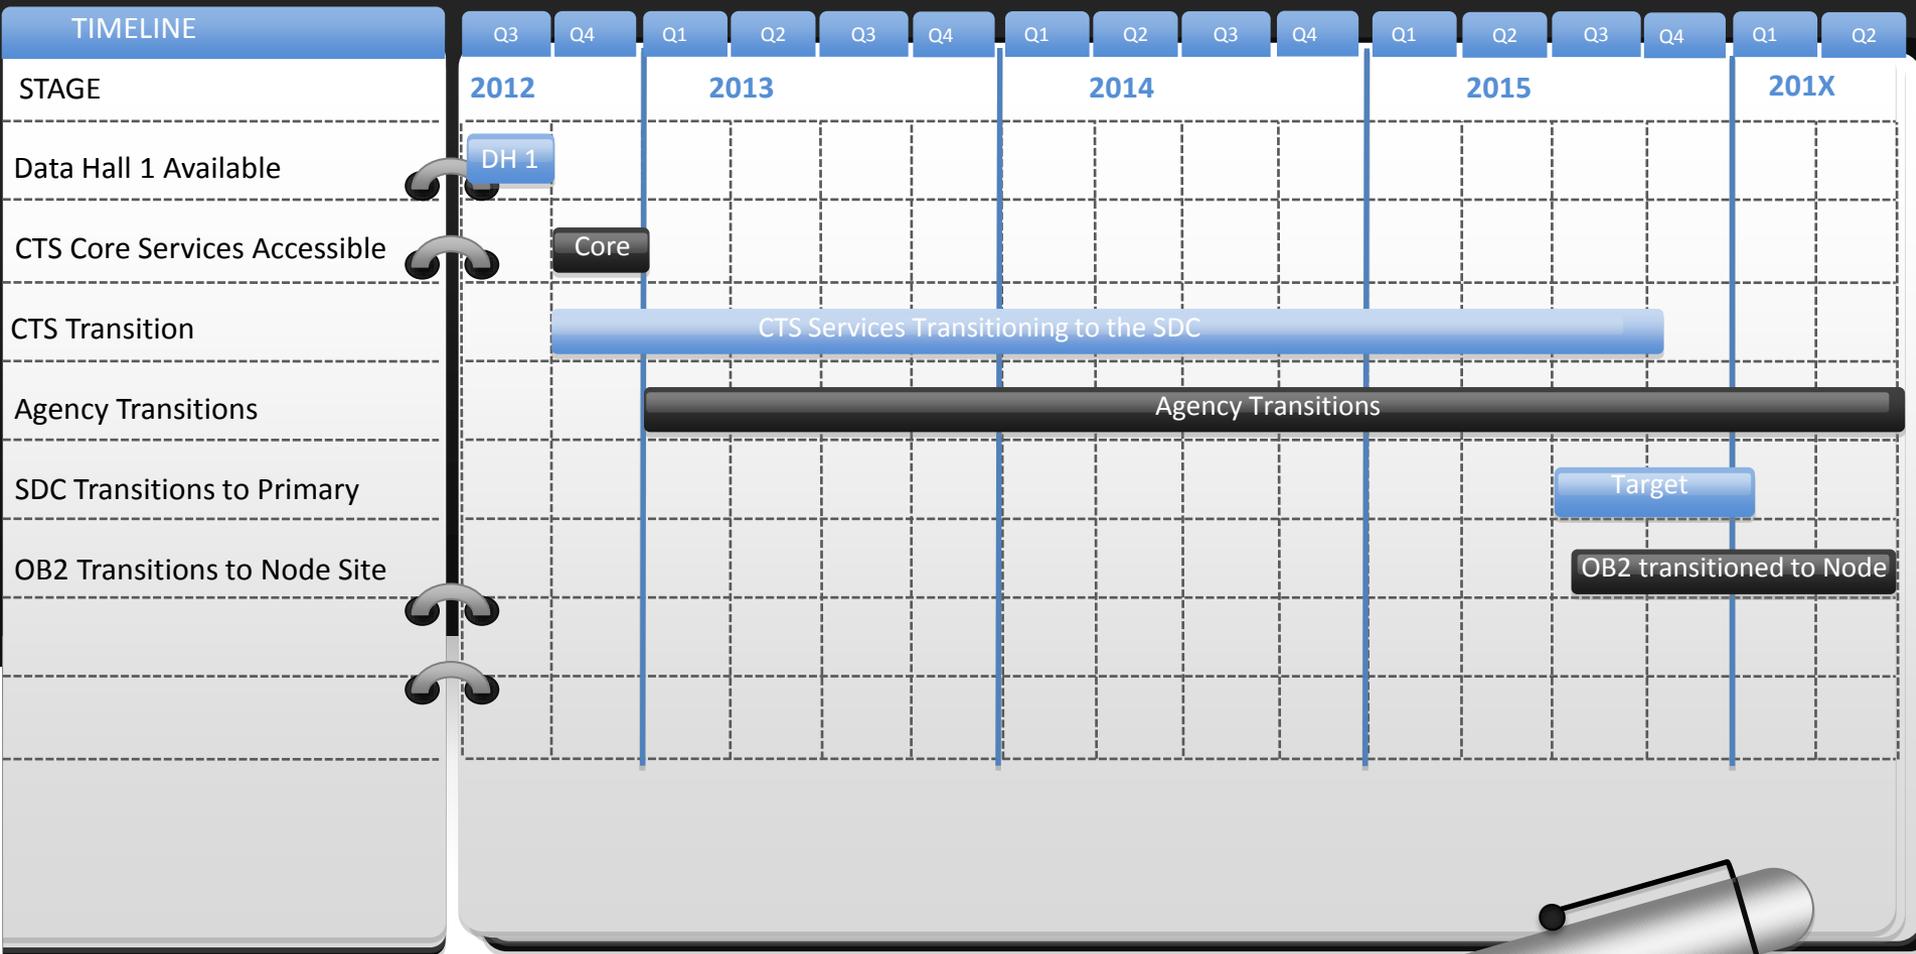

SDC ROADMAP 2012-201X

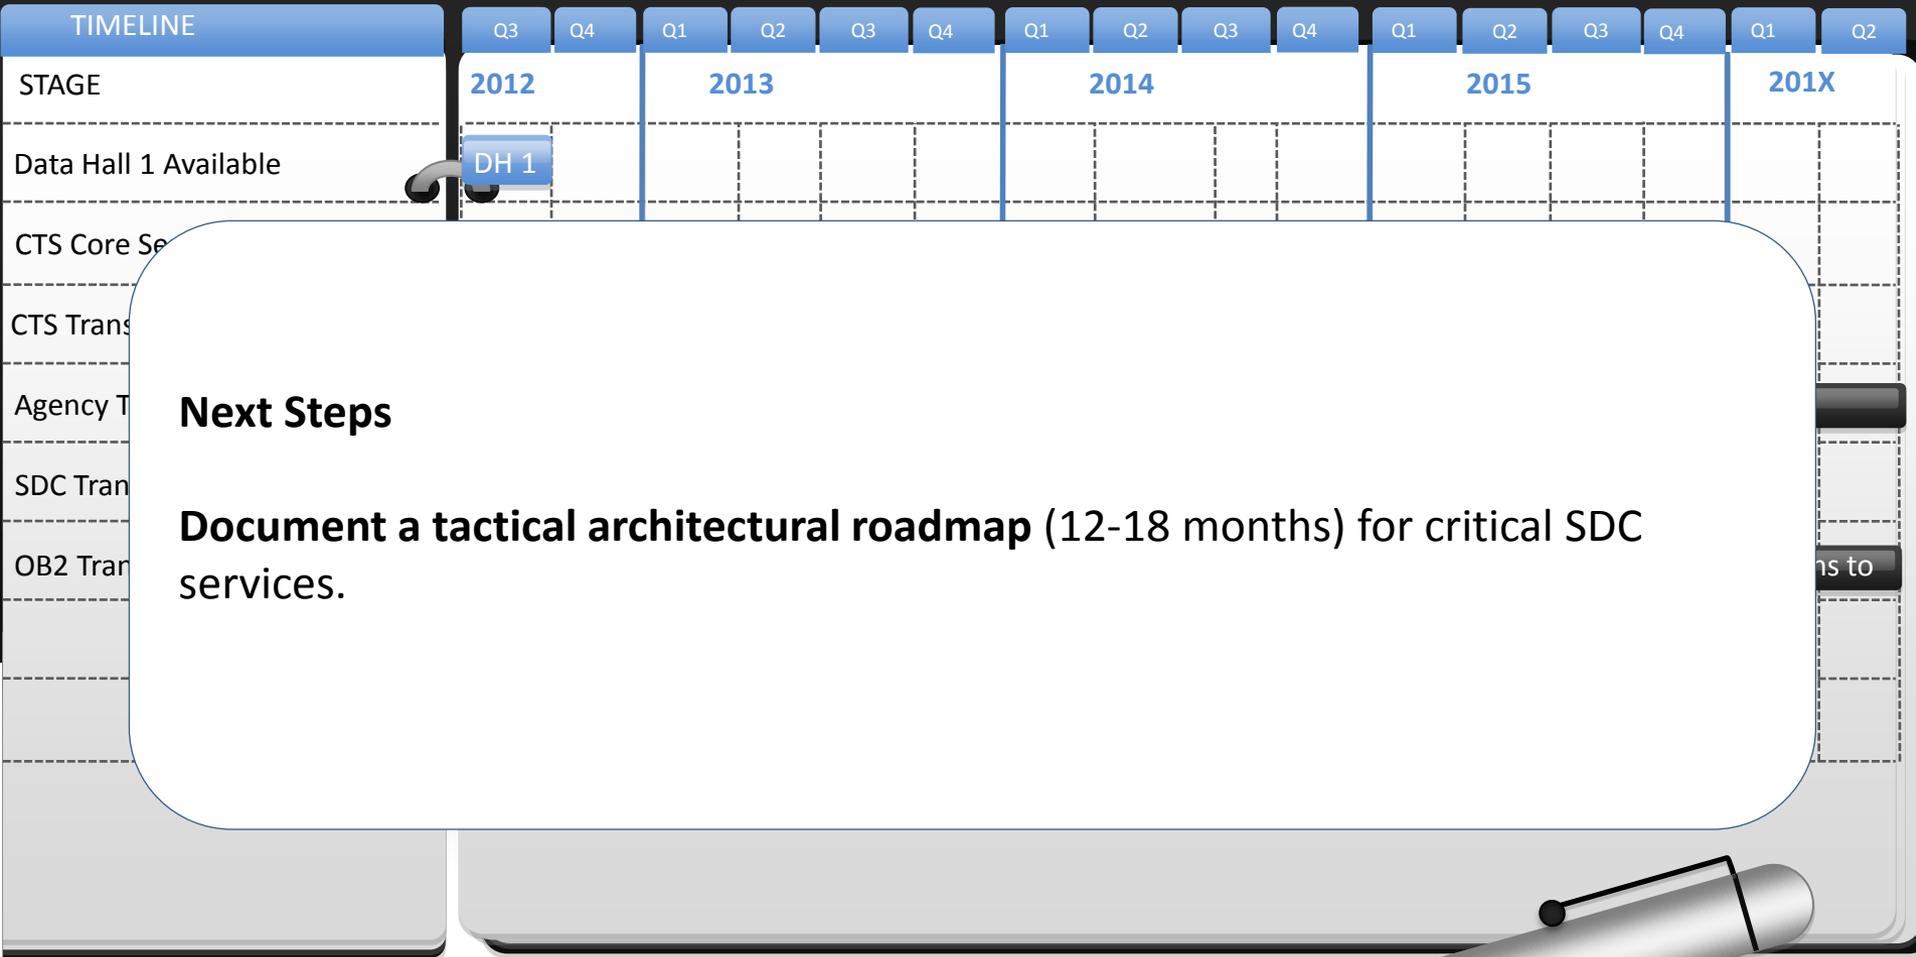

SDC ROADMAP 2012-201X

